



# Integrated Plan Implementation Quarterly Report

Q4 2023 (October 1 to December 31)  
and 2023 Annual Summary

March 14, 2024



# Meeting Agenda

- Call Meeting to Order: Chairman Currey
- Welcoming Remarks: Scott Jellison
- Introductions
- Meeting Purpose: to provide quarterly and annual update on MDC's Integrated Plan, with current focus on North Hartford
  - Quarterly Report from October 1, 2023 to December 31, 2023 (Q4 2023) and Annual Report of 2023 (July 1, 2023 to December 31, 2023)
    - An update on projects completed and under construction
    - A schedule for projects under construction or yet to start construction
    - A status of use of minority and disadvantaged business enterprises, including efforts and success at recruiting labor and contractors from the area where projects are or will be occurring
  - Next Quarterly Report Meeting = June 13, 2024 (Q1 2024)
- Public Comments and Questions

# Presentation Outline

- Background on focus area (North Hartford)
- Quarterly and Annual Consent Order reporting requirements
- Overview of Consent Order projects in:
  - North Hartford
  - Hartford (outside of North Hartford)
  - Outside Hartford
- Update on key performance indicators
- MDC's recruiting efforts for Small, Minority, Women and Disadvantaged Businesses (SBE, MBE, WBE, DBE) and Local Labor
- Clean Water Project Charge (CWPC) Update
- Closing remarks

# MDC Community Outreach Office

- MDC Commitment to North Hartford
  - Located at 179 Barbour Street, Hartford
- Outreach Office expected to be in use through late 2026 (minimum)
- MDC utilized local vendors for Office:
  - Plumber
  - Window Screening
  - Painting
- Ribbon-Cutting Planned for April 2024
- Office to be staffed as needed based on project activities in North Hartford

**MDC** The Metropolitan District  
 655 Main Street  
 Hartford, CT 06142  
 860.278.7850

Contact:  
 Nick Salemi  
 860.278.7850 Ext. 3211  
[nsalemi@themdc.com](mailto:nsalemi@themdc.com)

## MDC TO OPEN OUTREACH OFFICE TO SUPPORT NORTH HARTFORD SEWER IMPROVEMENT PROJECTS

*Community Outreach Office scheduled to open in February*

January 19, 2024  
 For Immediate Release

(HARTFORD, CT) – The Metropolitan District (MDC) announced today that the organization has recently secured a location for a dedicated Community Outreach Office at 179 Barbour Street in Hartford. The office will serve as a central hub for engaging with the local community and ensuring open lines of communication throughout the duration of the North Hartford Sewer Improvement Projects construction.

Recognizing the importance of this location to the community, the office will serve as a space for addressing concerns, providing project updates, and actively seeking feedback from residents and stakeholders as well as provide workforce development opportunities for the community. An official opening and ribbon cutting are planned for February with an open house to follow in the spring.

MDC's North Hartford Sewer Improvement Projects, a significant undertaking, began in July 2023. The work includes multiple sewer separation, rehabilitation and lining work to upgrade local infrastructure in North Hartford. Establishing a dedicated office will support current and future work and will further streamline communication channels and ensure that stakeholders are well-informed about the project's progress, potential disruptions, and any necessary information.

MDC has two active sewer separation projects that have already seen significant progress, one on Durham Street (24 properties) and the other on Woodstock and Branford Streets (72 properties) with another to begin this year on Westland Street (126 properties). In addition, a Sewer Rehabilitation and Lining project in the year in the Granby/Blue Hills, North Hartford resident workforce goal.

venience and disruption to the local living local outreach offices for that residents have a place to actively in our construction area neighborhood I want to recognize community leader take this happen."

available in the coming weeks.

in Connecticut General Assembly in its member towns: Bloomfield, East Windsor

[WWW.THEMDC.ORG](http://WWW.THEMDC.ORG)




# The North Hartford Area

Focus is:


- Sewer separation: remove public and private stormwater from sewer system
- Private property sewer work (which was not the prior focus)
- Reduce flooding
- Reduce sewer surcharge
- Reduce private property backups
- Reduce CSOs to rivers

**MDC listened to the North Hartford Community and responded with an altered program that provides immediate community benefit**


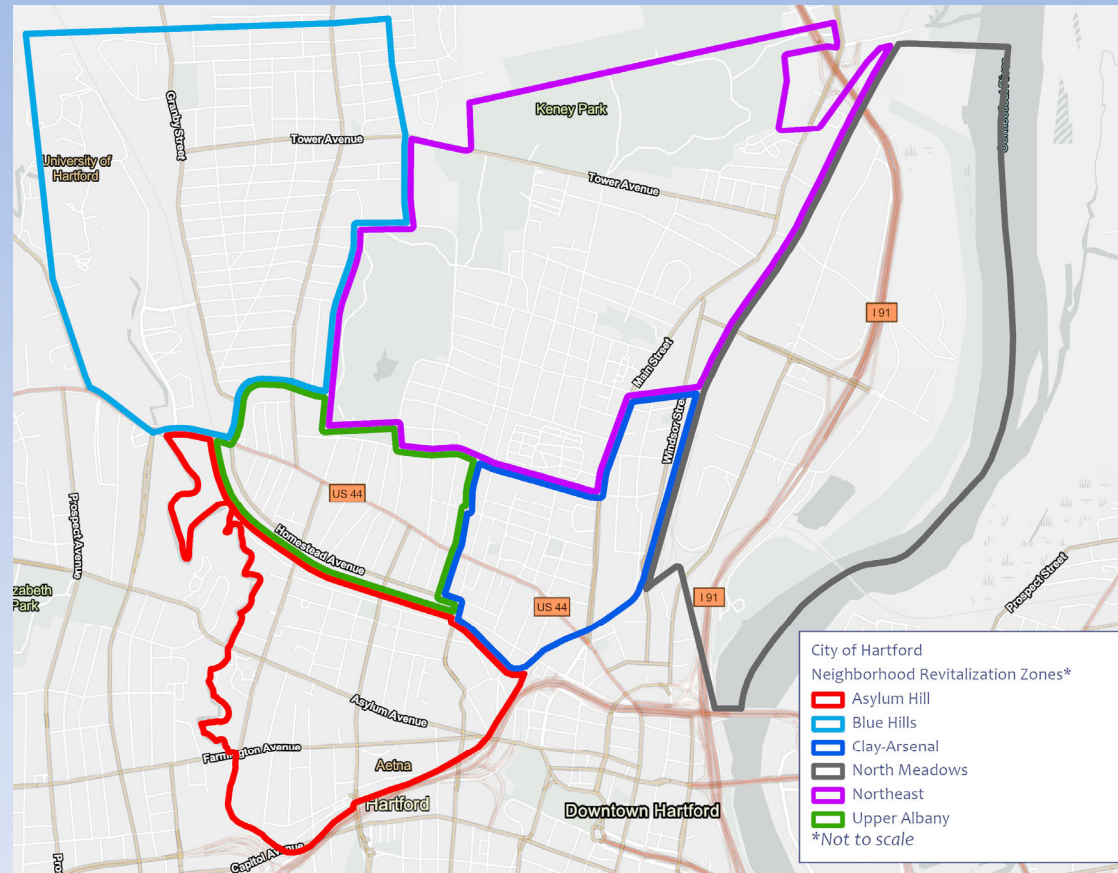


# Community Benefit: Private Property Improvements

**BWV/PPID**

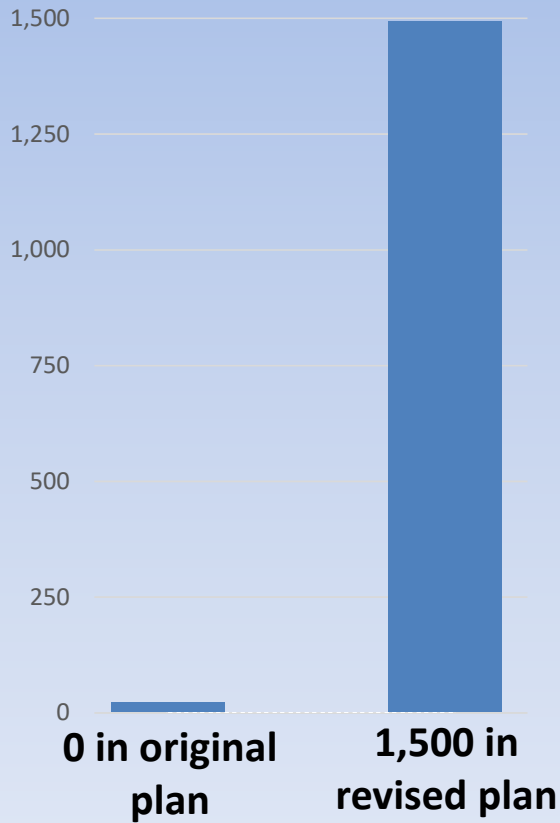

**Lateral Renewal/  
Replacement**

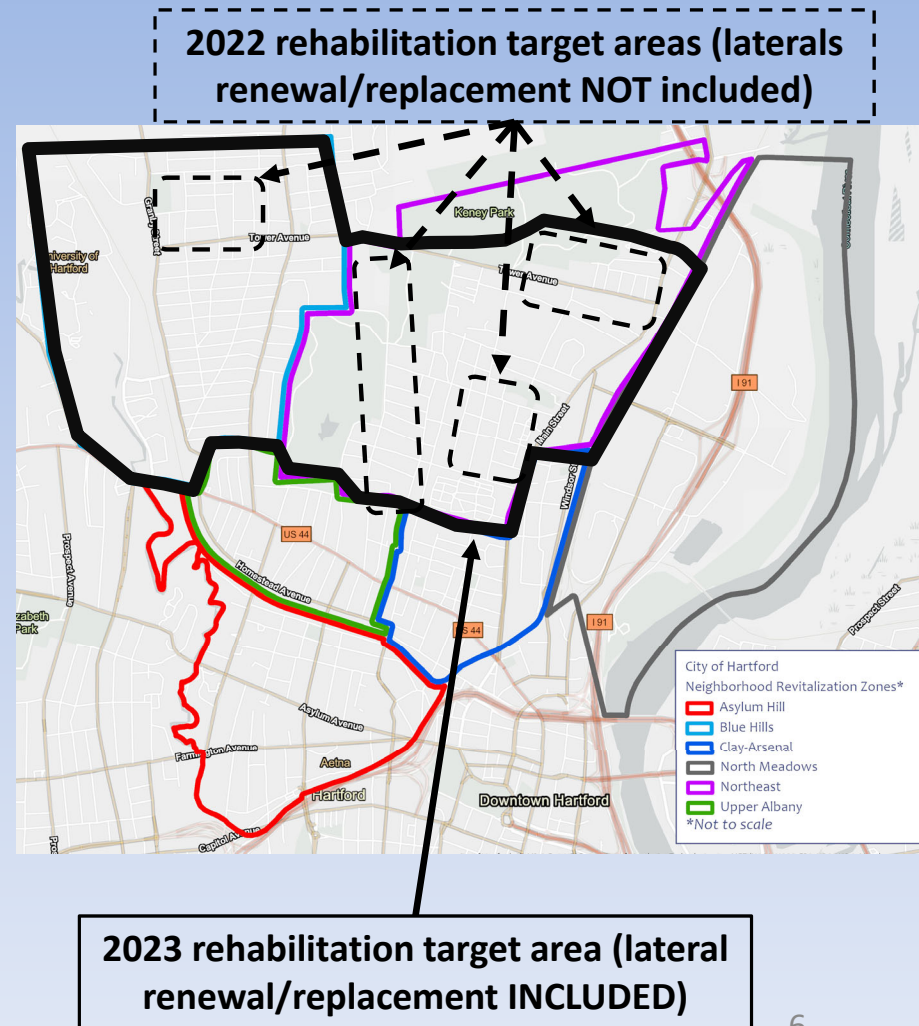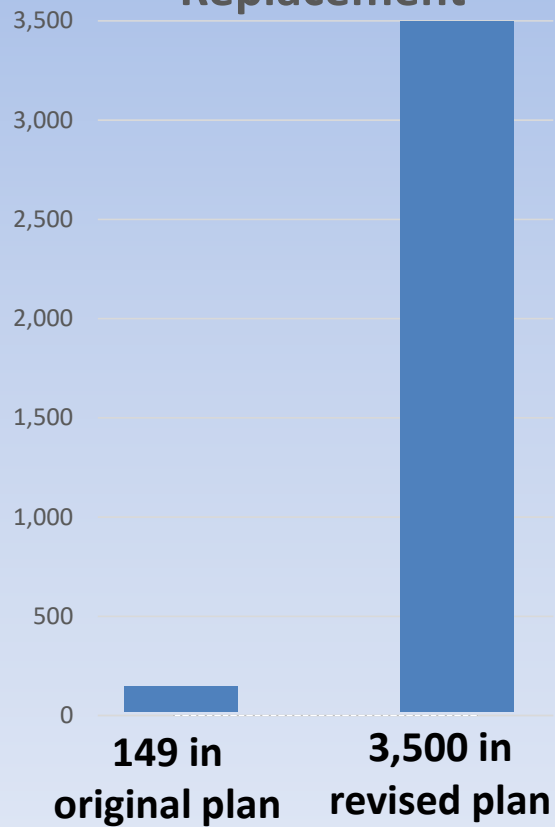

# Consent Order Modification Reporting Requirements


## Quarterly and Annual Reporting Required under Consent Order Modification

- **Draft Report posted on MDC website on February 14, 2014**
  - Posted 30 Days Prior to Meeting (CO Requirement)
  - Report submitted to both CT DEEP & ICA
    - Comments received & incorporated into presentation
- **Separate Report from monthly progress reports required per Public Act 23-204**
  - Reports posted on MDC Website
- **Per Consent Order, Report must include the following:**
  - An update on projects completed and under construction
  - A schedule for projects under construction or yet to start construction
  - A status of use of minority and disadvantaged business enterprises, including efforts and success at recruiting labor and contractors from the area where projects are or will be occurring
  - Other items as requested by Commissioner
    - *Not applicable for this quarter*

## Other Items Voluntarily Included by the MDC

- MDC committed to 30% Hartford based workforce for North Hartford work associated with Consent Order modification
  - 30% based on similar City of Hartford goal on municipal projects

# Consent Order Projects & Timeline

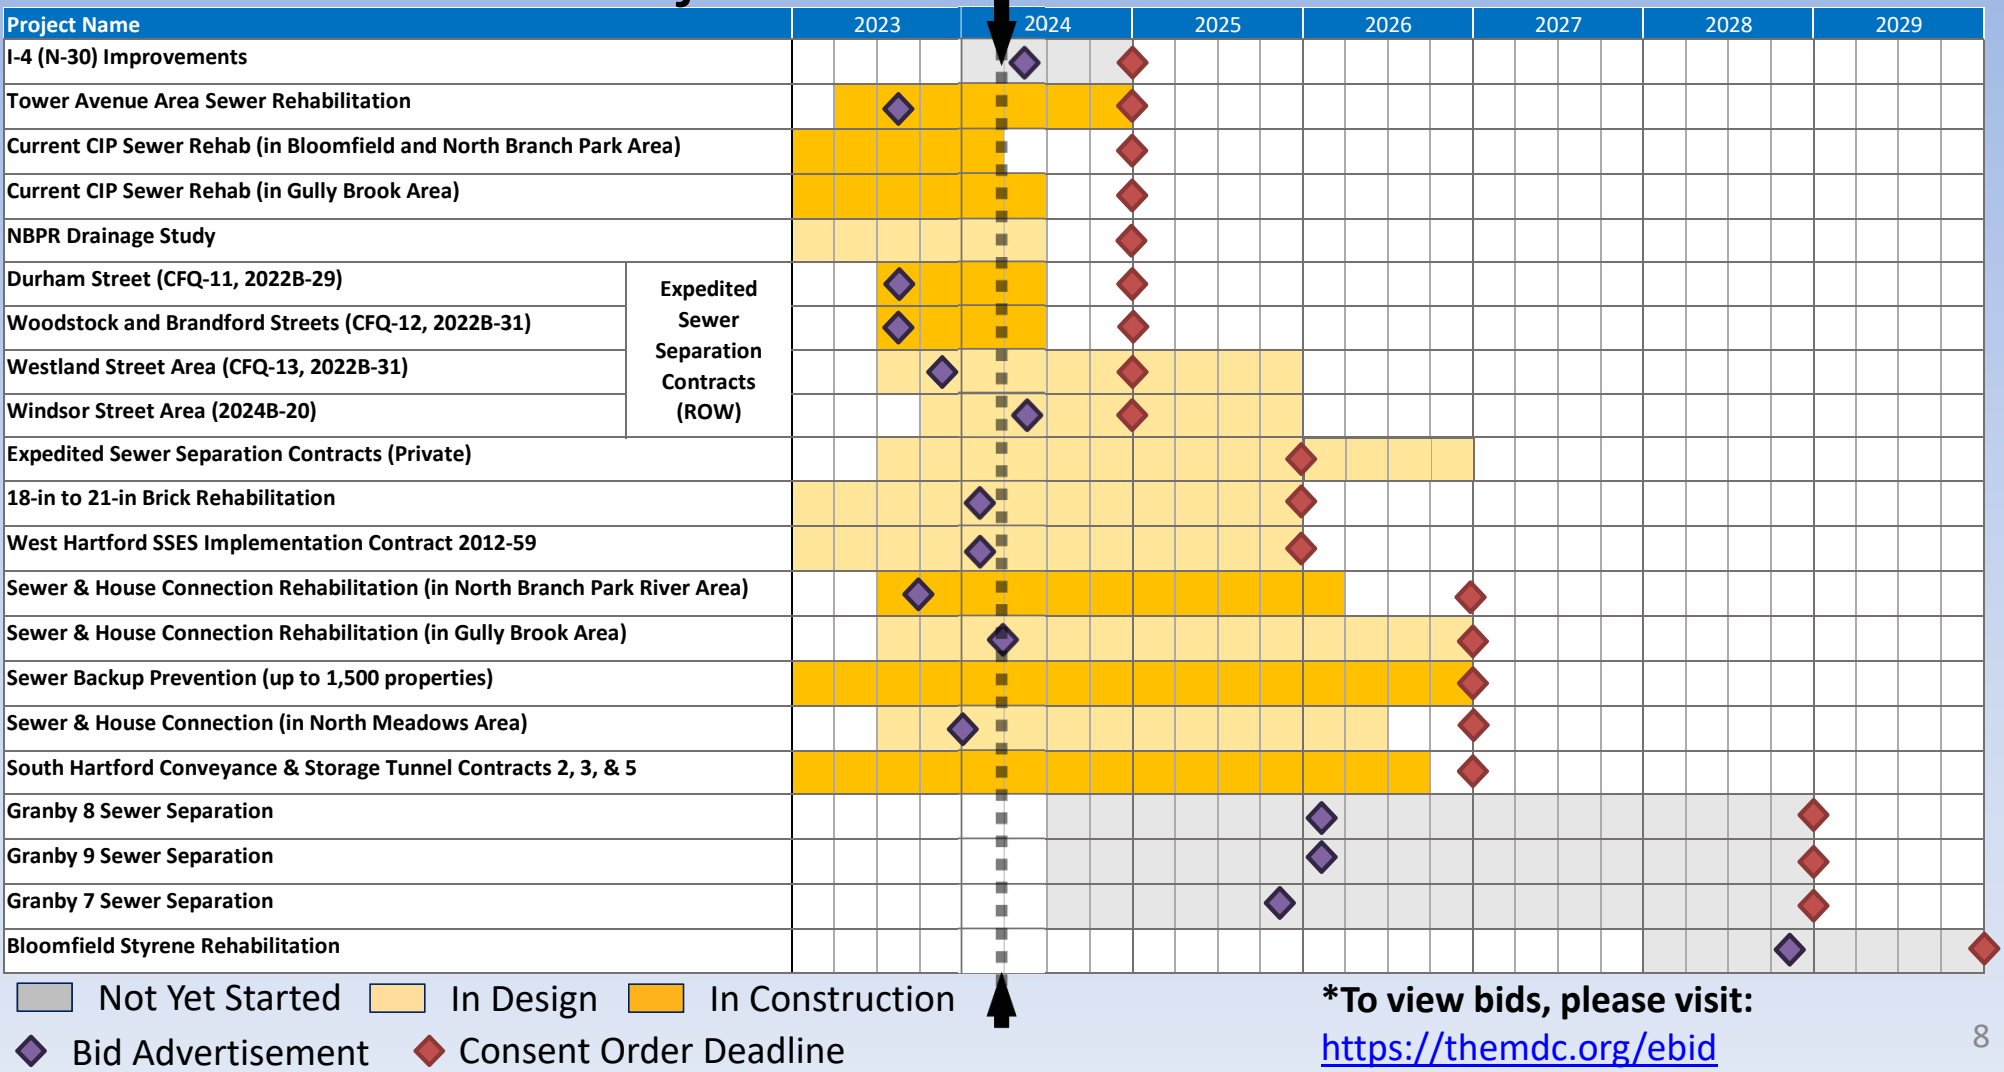

**\*To view bids, please visit:**  
<https://themdc.org/ebid>



# Expedited Sewer Separation Program – Schedule Update


- Existing CO Milestone Dates:
  - Single Milestones for Multiple “Projects”
    - ROW Work = 12/31/24
    - Private Property Work = 12/31/25
- CO Scope:
  - ROW Work = Installation of up to 8,000 LF of new storm drains & associated laterals
  - Private Property Work = Separation work at up to 160 properties
  - Preliminary Plan of Streets:
    - Branford Street (between Blue Hills Avenue & Coventry Street) & Woodstock Street (entire street)
    - Durham Street (entire street)
    - Westland Street (between Love Lane & Clark Street)
    - Windsor Street (between Main Street & Sanford Street)

# Expedited Sewer Separation Program – Schedule Update

- **Scope Additions:**
  - Westland Street Area Project:
    - Added Garden Street (between Capen Street & Charlotte Street)
    - Added Risley Street (entire street)
  - Windsor Street Area Project:
    - Added Main Street (between Windsor Street & Cleveland Avenue)
  - Additional 1,320 LF of storm drains & associated laterals
  - Additional 1,730 LF of new sanitary sewers & associated laterals (to facilitate separation)
  - Additional 97 properties (60% increase) to be included in separation program
- **Utility Conflicts:**
  - Westland Street Area Project:
    - Relocations of Water Mains & CNG Pipelines required for new storm drains and sanitary sewers
  - Windsor Street Area Project:
    - Relocation of Frontier Communications conduits required for new storm drains
- **Additional Water Main Work:**
  - 730 LF of water main replaced on Durham Street in advance of storm drain installation
  - 1,450 LF of water main replaced on Branford Street in advance of storm drain installation
  - 1,475 LF of water main replacement included in the Westland Street Area Project in conjunction with storm drain and other water main relocation work.

# Expedited Sewer Separation Program – Schedule Update

- Project Specific Schedules:
  - Durham Street:
    - ROW work completed in February 2024, with restoration to follow
    - Private property work to be complete by end of 2024
    - **No schedule extension required**
  - Branford & Woodstock Streets:
    - ROW work to be complete mid-2024
    - Private property work to be complete by mid-2025
    - **No schedule extension required**
  - Westland Street Area:
    - ROW work to be complete by Fall 2025
    - Private property work to be complete by end of 2026
    - **Requires schedule extension**
  - Windsor Street Area:
    - ROW work to be complete by Fall 2025
    - Private property work to be complete by end of 2026
    - **Requires schedule extension**
- Schedule Update Request:
  - ROW work = 12/31/25
  - Private Property work = 12/31/26

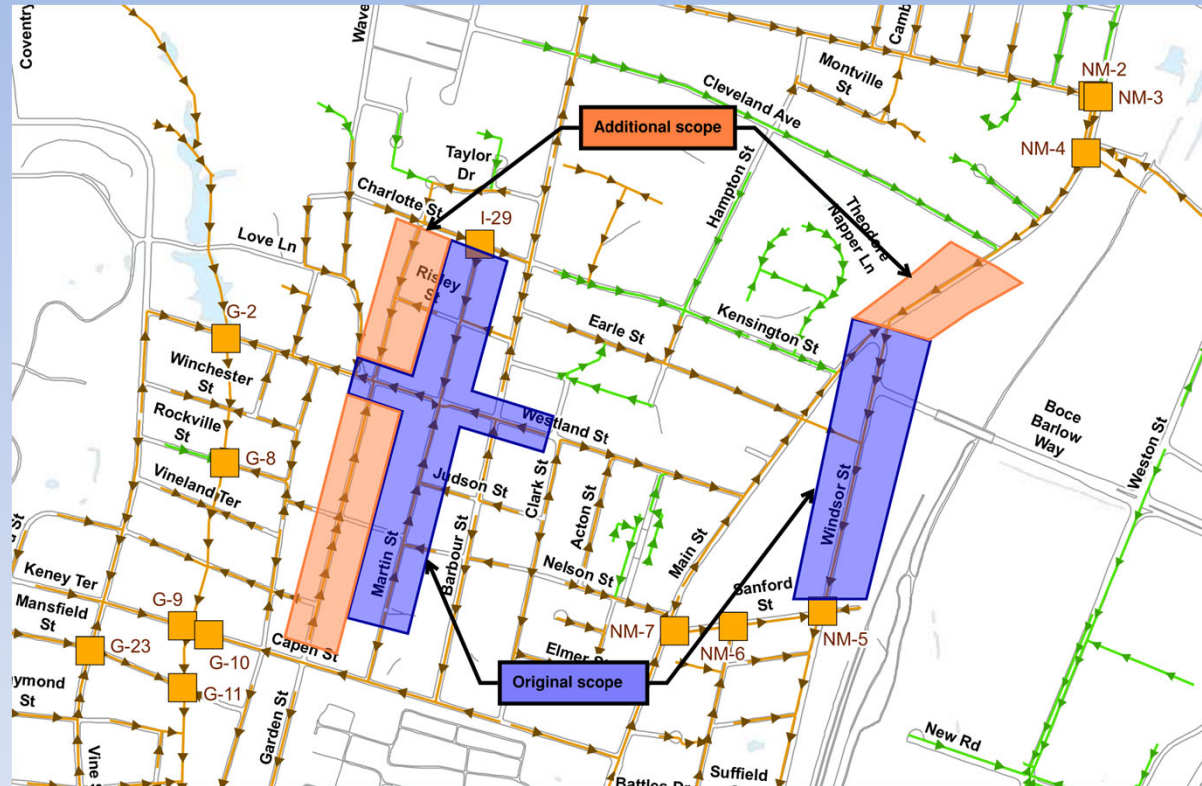

# Consent Order Projects: NRZ Impact and CSO Reduction

Project Name	Neighborhood Revitalization Zone	1 Yr CSO Reduction (MG)	Typical Year CSO Reduction (MG)
I-4 (N-30) Improvements	West End	<0.1	<0.1
Tower Avenue Area Sewer Rehabilitation	North East	0.2	3.0
Current CIP Sewer Rehab (in Bloomfield and North Branch Park Area)	Blue Hills, Clay Arsenal, South Downtown, South Behind the Rocks	0.2	2.4
Current CIP Sewer Rehab (in Gully Brook Area)	Clay Arsenal, Asylum Hill, South Behind the Rocks	1.3	10.0
NBPR Drainage Study	Blue Hills, West End, Asylum Hill	*	*
Durham Street (CFQ-11, 2022B-29)	Expedited Sewer Separation Contracts (ROW)	Blue Hills	1.2
Woodstock and Brandford Streets (CFQ-12, 2022B-31)		Blue Hills	1.4
Westland Street Area (CFQ-13, 2022B-31)		Northeast	2.9
Windsor Street Area (2024B-20)		North Meadows	14.3
Expedited Sewer Separation Contracts (Private)	Various	*	*
18-in to 21-in Brick Rehabilitation	Asylum Hill, Clay Arsenal, South End, Marg	0.8	7.0
West Hartford SSES Implementation Contract 2012-59	N/A	0.2	1.2
Sewer & House Connection Rehabilitation (in North Branch Park River Area)	Blue Hills	0.9	11.5
Sewer & House Connection Rehabilitation (in Gully Brook Area)	Northeast	0.9	11.0
Sewer Backup Prevention (up to 1,500 properties)	Various	**	**
Sewer & House Connection (in North Meadows Area)	North Meadows	1.0	28.4
South Hartford Conveyance & Storage Tunnel Contracts 2, 3, & 5	South End, Marg, South Behind the Rocks	3.8	21.9
Granby 8 Sewer Separation	Blue Hills	0.3	3.4
Granby 9 Sewer Separation	Blue Hills	0.4	3.6
Granby 7 Sewer Separation	Blue Hills	0.4	3.8
Bloomfield Styrene Rehabilitation	N/A	<0.1	<0.1

\*CSO Reductions for the NBPR Drainage Study included in individual Granby Separation Contracts


\*\* CSO Reductions associated with Private Property Improvements included in associated ROW Project Reduction Estimates

# Additional Sewer Improvement Projects

*Non-Consent Order (2019 through Q4 2023)*

- **Clearing Sewer Easements on Private Property**
  - Completed = Bloomfield, Rocky Hill, East Hartford, Windsor
  - In progress = Newington
  - Other Member Towns to follow
- **Easement Sewer Rehabilitation**
  - Bloomfield currently
  - Other Member Towns to be evaluated/scheduled
- **On-Call Sewer Rehabilitation/Repair**
  - 230,000 feet rehabilitated from 2019 to 2023
  - Performed in all Member Towns
    - In Q4: work performed in Bloomfield, East Hartford, Hartford, West Hartford
  - Asset management/paving program coordination

Town	Easement Clearing Length (feet)
Bloomfield	98,000 (completed)
Rocky Hill	59,100 (completed)
East Hartford	66,200 (completed)
Windsor	132,300 (completed)
Newington	51,300 (in progress)
Hartford	55,800
West Hartford	54,300
Wethersfield	59,200
<b>Total (feet)</b>	<b>576,000</b>
<b>Total (miles)</b>	<b>109</b>

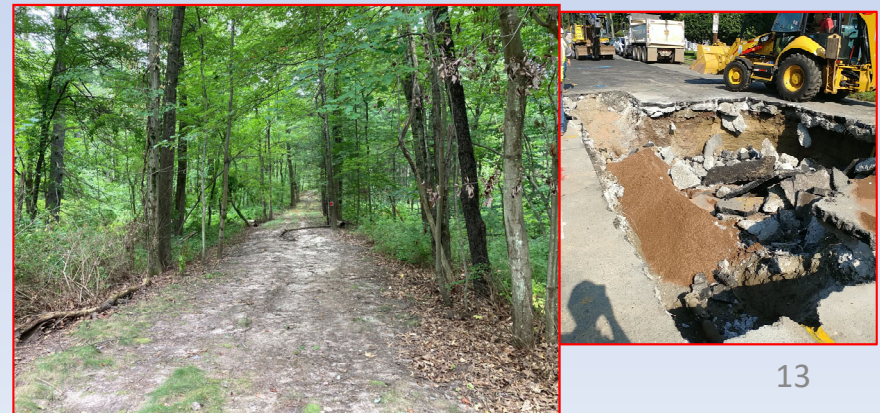

# Consent Order Projects: North Hartford

**North Branch Park River Area  
Sewer Rehabilitation:**

Rehabilitation of sewer mains and house connections upstream of CSOs N-2 and N-4

**Expedited Sewer Separation  
Contracts (ROW):**

Construction of storm drains in streets  
**(Additional separation added per MDC review)**

**Expedited Sewer Separation  
Contracts (Private):**

Private property storm separation (to follow Public Separation Contracts)

**North Branch Park River  
Drainage Study:**

Evaluating the North Branch Park River and surrounding sewer and drainage infrastructure in support of future river improvements and sewer separation

**Granby 7/8/9 Sewer Separation:**  
Sewer separation with new storm drains and private property disconnections (final location based on North Branch Park River Study)

**Tower Avenue Area  
Sewer Rehabilitation:**




Rehabilitation of sewer mains and house connections upstream of CSOs NM-2, NM-3, and NM-4

**North Meadows Area  
Sewer Rehabilitation:**

Rehabilitation of sewer mains and house connections upstream of CSOs NM-5, NM-6, and NM-7

**Gully Brook Area  
Sewer Rehabilitation:**


Rehabilitation of sewer mains and house connections upstream of CSO G-13W

-  Not Yet Started
-  In Design
-  In Construction

# Consent Order Projects: Private Property Benefit


## Sewer Backup Prevention Program (“Backwater Valve Program”)

- Separates homes’ foundation drains (via installing sump pumps) and gutters from the sewer system, reducing surcharging during wet weather
- \$12.2 million (up to 1,500 homes) for North Hartford properties (Consent Order project)
- <https://themdc.org/utility-services/backwater-valve-program/>
- To **schedule a free assessment** of your property, contact MDC Utility Services at **(860) 278-7850, ext. 3123**

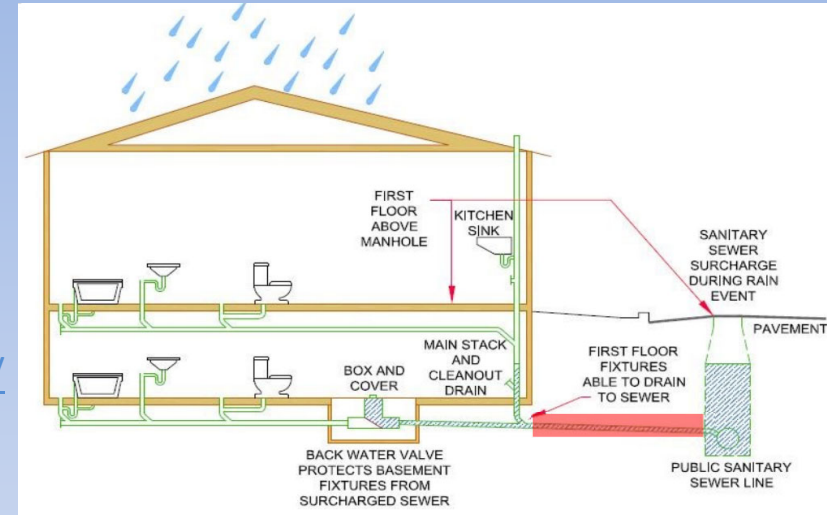

## House Connection Program – voluntarily included by MDC

- MDC Board initiative to provide same benefit District-wide that was being offered to North Hartford residents
- Emergency and non-emergency maintenance and inspection services at no cost to the property owner
- Provides funding for renewal of the house connection, if needed
- <https://themdc.org/utility-services/sewer-house-connection-program/>

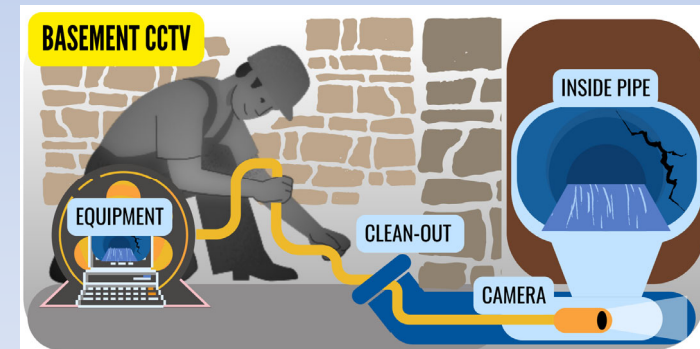


Contractors for both programs are anticipated to be all SBE (Small Business Enterprise)

# Private Property Benefit: House Connection Lining

- House Connection (“lateral”) Lining is a two-step process:
  - Lining from mainline sewer to a the connection with building plumbing (**Green** Portion)
  - Lining of building plumbing from a basement cleanout to the house connection (**Blue & Red** Portions)
- Signed Agreements required for All Private Property Work
- MDC will line House Connection from mainline sewer & then schedule lining from basement cleanout (typically within 3 months)

Portion in blue is the building plumbing exiting the foundation (typically cast iron and 4 inches in size) connecting to the larger house connection pipe

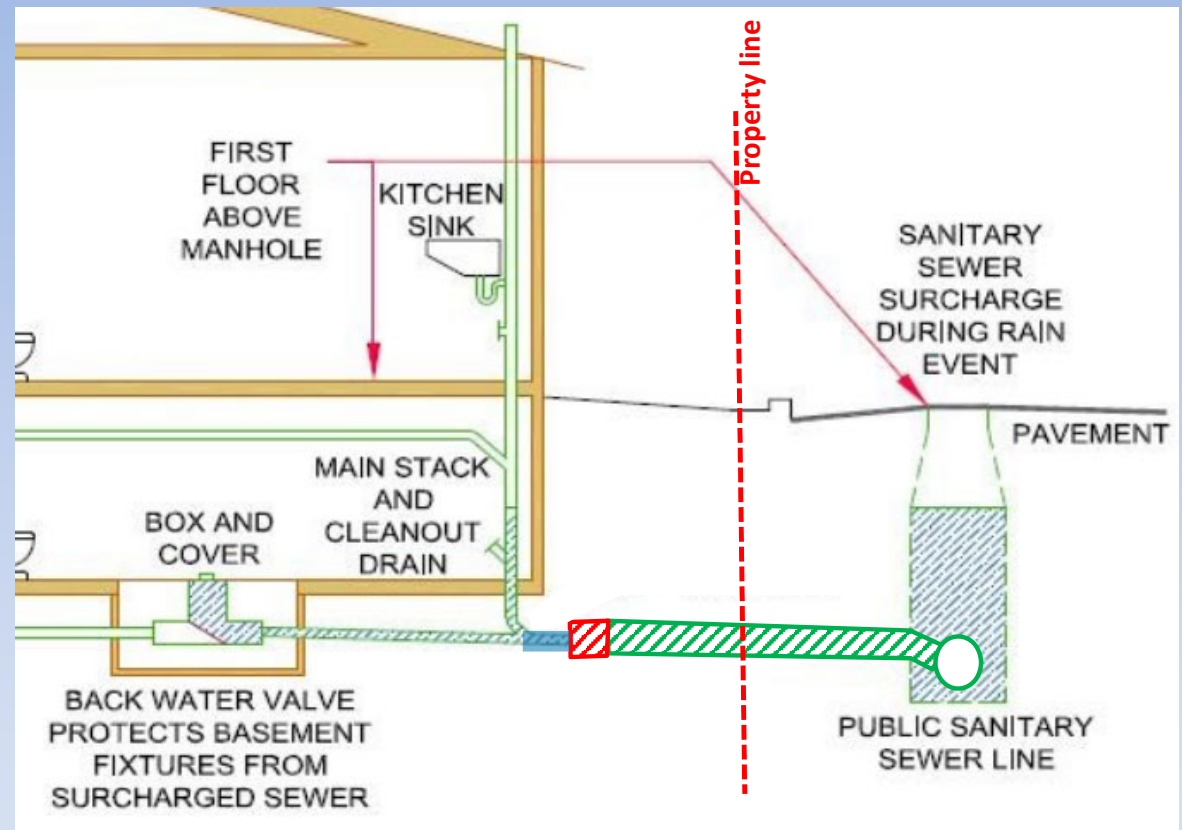

Portion of house connection that is typically 6 to 8 inches in size. Portion in green is typically lined from the sanitary sewer line, portion in red is where the larger part of the house connection connects to the smaller internal plumbing house connection and cannot be lined from the public sanitary sewer due to lining technology limitations



# Consent Order Projects: Outside of North Hartford

## Gully Brook Area Sewer Rehabilitation:

Rehabilitation of sewer mains and house connections

## Bloomfield and North Branch Park River Area Sewer Rehabilitation:

Rehabilitation of sewer mains and house connections

## 18-in to 21-in Brick Rehabilitation:



Rehabilitation of brick sewer mains

## I-4 (N-30) Improvements:

Rehabilitation of sewer mains downstream of CSO I-4 (N-30)


## South Hartford Conveyance & Storage Tunnel (SHCST) Contracts 2, 3, & 5:

Construction of the SHCST, drop shafts, consolidation conduits and dewatering pumpstation

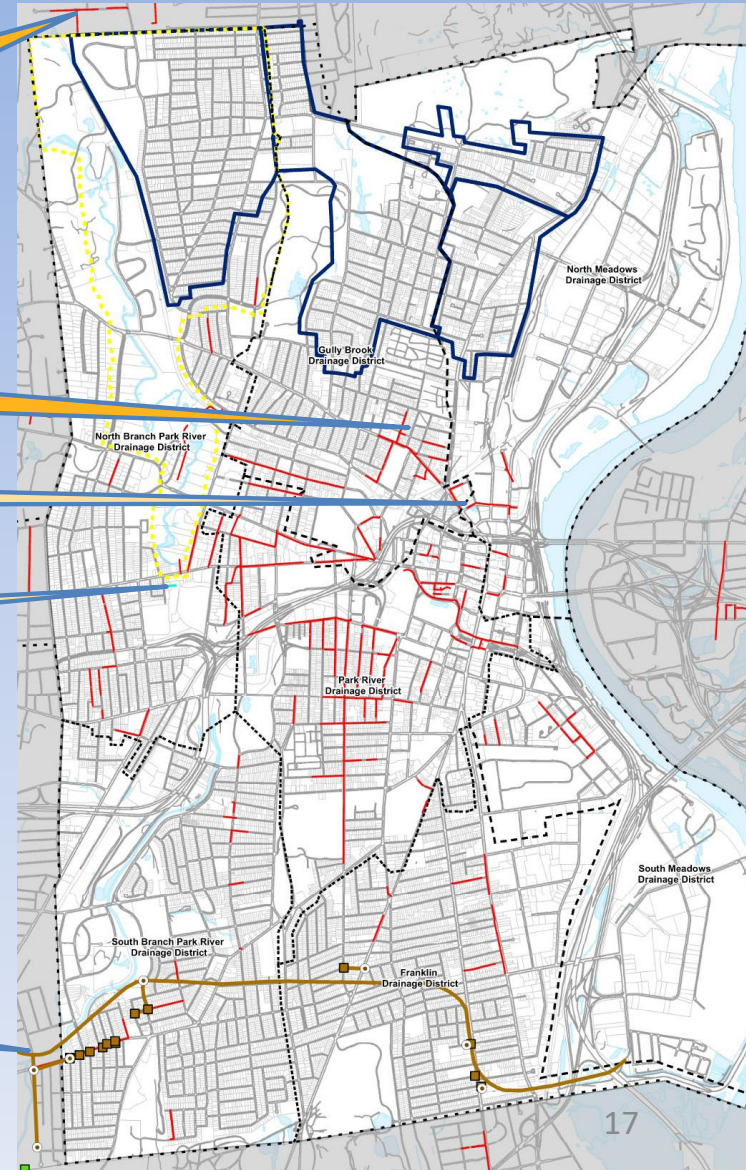


Not Yet Started   In Design   In Construction

# Consent Order Projects Locations: Outside of Hartford

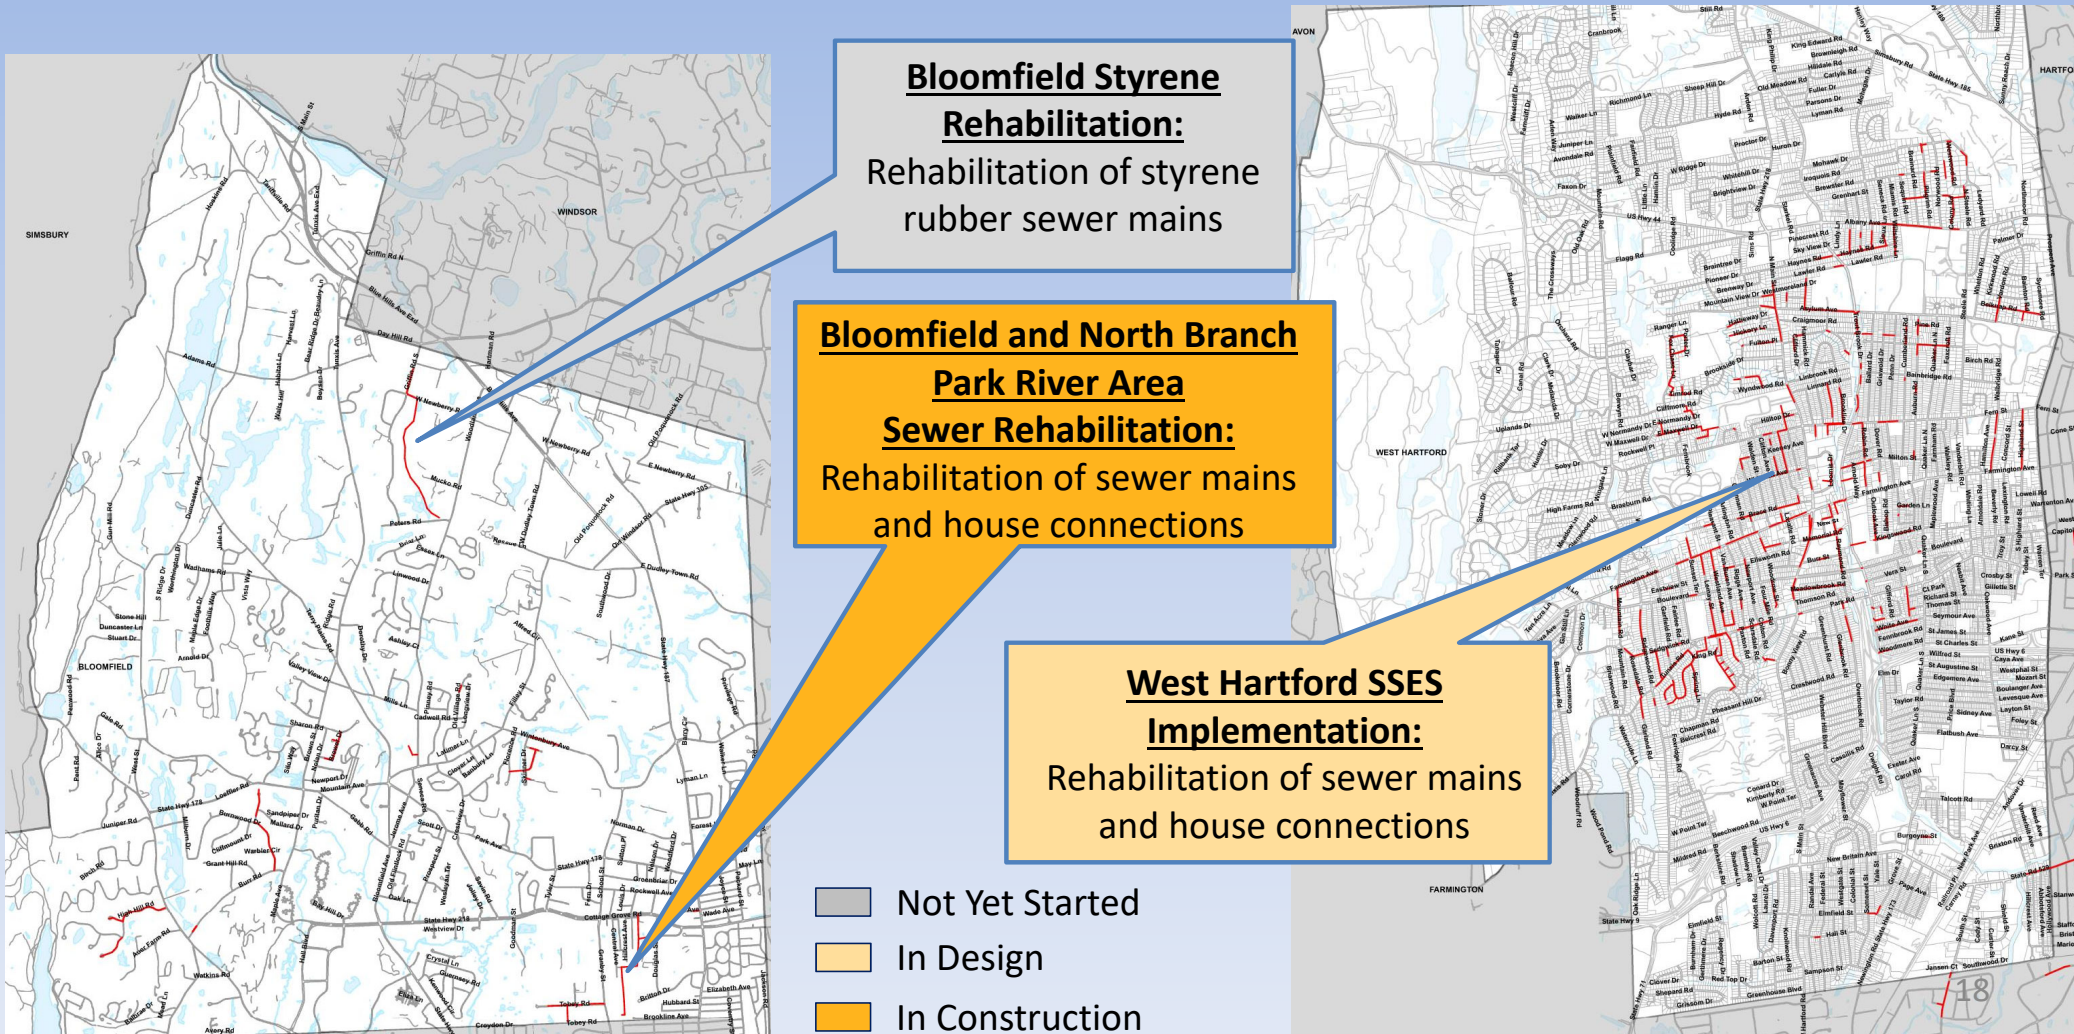

# North Branch Park River Drainage Study Update

- Importance of Study
  - NBPR has sediment buildup (i.e., from streets) and blockages (i.e., from downed trees); needs attention as these contribute to street and localized flooding and backups
- Study needed to determine
  - Required flood control and stream improvements (COH priority)
  - Approach to remove stormwater from sewers to eliminate CSOs (MDC priority)
- River assessment ongoing
- Short term improvements performed
  - City cleaned Park River Conduit inlet
- Durham Street sewer separation ongoing
- Conceptual sewer separation design underway
- Study to be completed in 2024

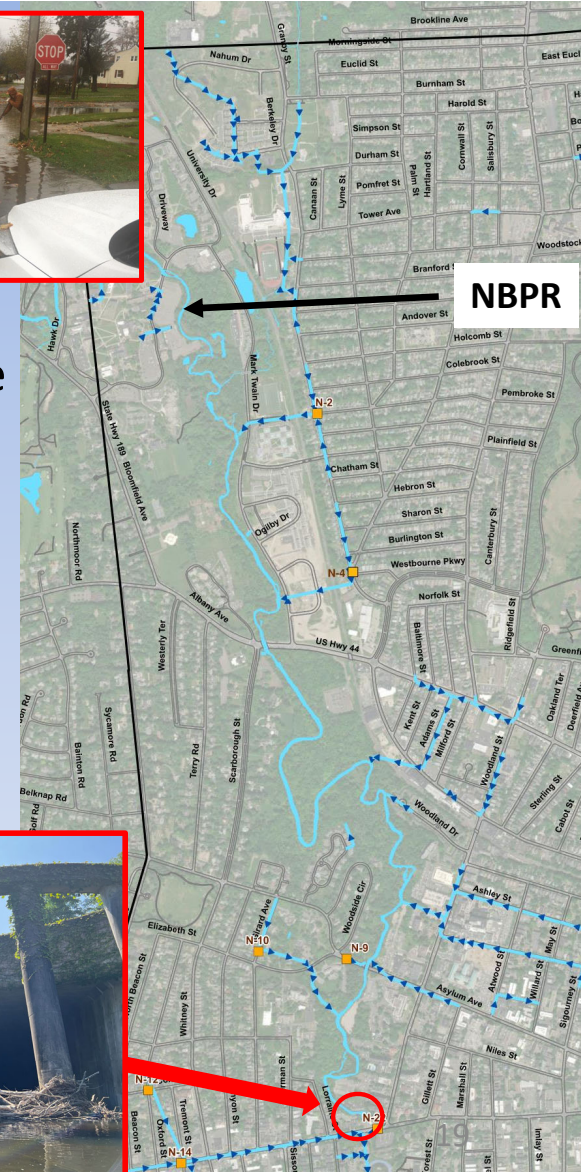

# Status of Projects: Key Performance Indicators (District Wide\*)



Key Performance Indicators	Q4 2023 (Oct 1 through Dec 31)	2023 Annual (July 1 through Dec 31)	Total To Date (since 2019)
Storm drains or sanitary sewers installed (feet)	1,631'	2,531'	31,631'
Sewer or storm laterals installed via separation (# of properties)	0	0	0
Sewer mains rehabilitated (feet) (miles)	35,773' (6.8)	64,773' (12.3)	323,773' (61.3)
Sewer laterals inspected (# of properties)	592	1,392	3,192
Sewer laterals renewed (# of properties) (feet)	301 (9,739')	371 (11,739')	381 (12,239')
Backwater valve/surcharge protection (# of properties)	155	235	1,017
Private property internal disconnects (# of properties)	53	72	111
Private property separation completed (# of properties)	0	0	0

\*Work in all Member Towns, including North Hartford

# Status of Projects: Key Performance Indicators (North Hartford)



Key Performance Indicators	Q4 2023 (Oct 1 through Dec 31)	2023 Annual (July 1 through Dec 31)	Total To Date (since 2019)
Storm drains or sanitary sewers installed (feet)	1,631'	2,181'	9,131'
Sewer or storm laterals installed via separation (# of properties)	0	0	0
Sewer mains rehabilitated (feet) (miles)	12,869' (2.4)	14,369' (2.7)	37,869' (7.2)
Sewer laterals inspected (# of properties)	173	373	423
Sewer laterals renewed (# of properties) (feet)	97 (4,415')	97 (4,415')	101 (4,565')
Backwater valve/surcharge protection (# of properties)	61	101	346
Private property internal disconnects (# of properties)	25	38	57
Private property separation completed (# of properties)	0	0	0

# Status of Projects: N-2 and N-4 CSO Reduction

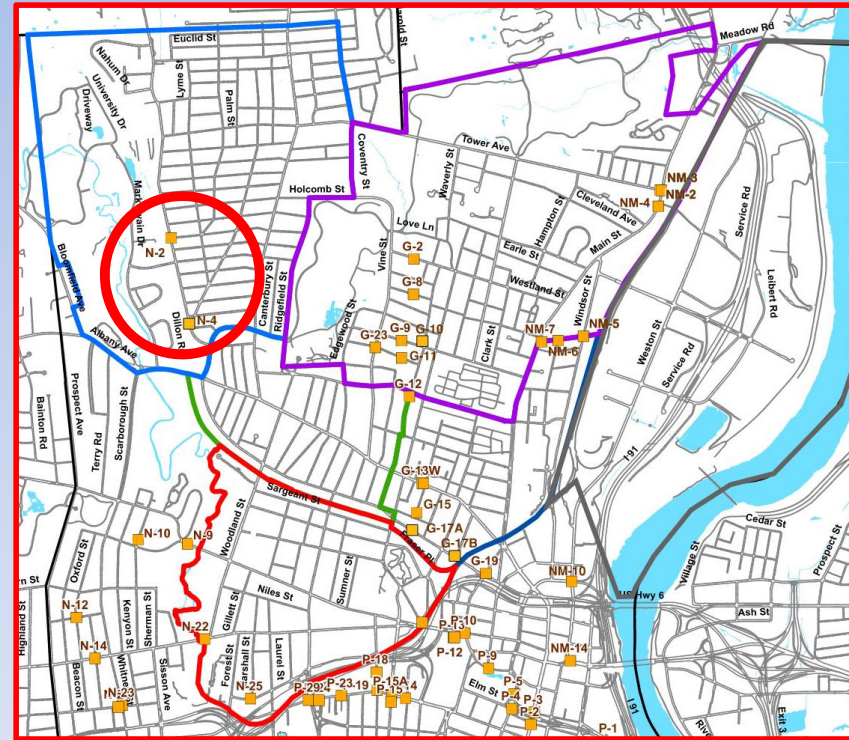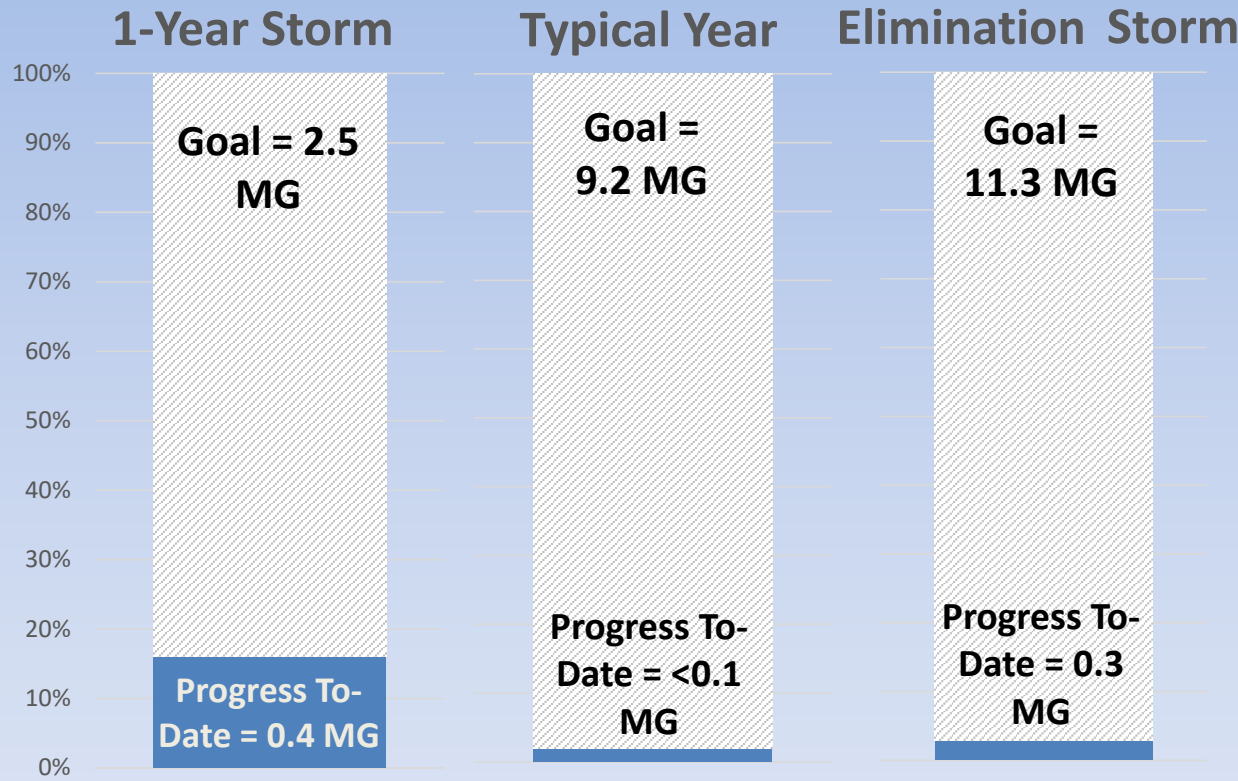

**Notes:** Per the Consent Order, combined sewer overflows (CSOs) from N-2 and N-4 must be eliminated. Million gallon (MG) goals are per 2018 Integrated Plan.

# Status of Projects: Gully Brook & North Meadows CSO Reduction

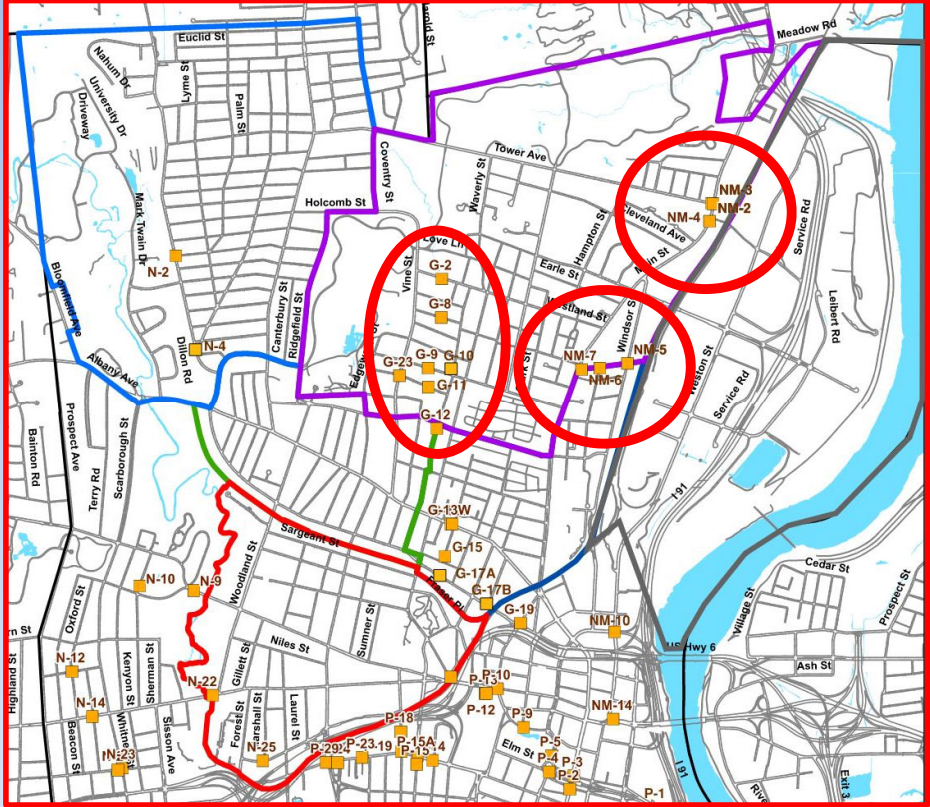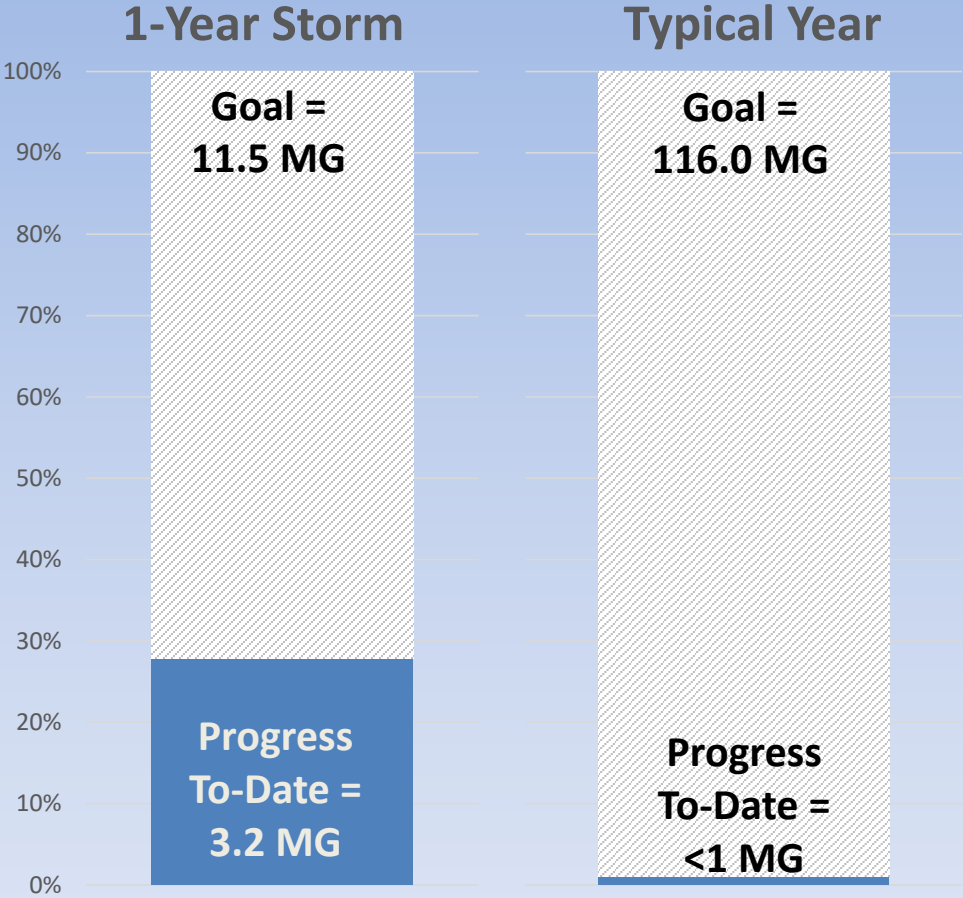

**Notes:** Per the Consent Order, CSOs from Gully Brook and North Meadows must be controlled to the 1-year storm. Goal represents the total million gallon (MG) of CSO that occurs in a 1-year storm and typical year.

# MDC's Recruiting Efforts for Small, Minority, Women and Disadvantaged Businesses (SBE, MBE, WBE, DBE)

- CT Department of Administrative Services (DAS) SBE/MBE/WBE and SAM.gov Registration Clinic with CT Apex Accelerator, National Association of Women in Construction (NAWIC), and University of Hartford
  - MDC Training Facility – October 18<sup>th</sup> and November 15<sup>th</sup>
  - Reviewed new applications
    - Assisted Contractors with recertification application
    - Q&A for new SAM.gov ID process
- Solicited targeted pre-bid attendance for second round of proposal submission from SBE/MBE/WBE Contractor's – City of Hartford MBE/WBE List, and CT DAS Vendor Search
- Advertised request for qualifications (RFQ) for Backwater Valve and House Connection Programs in Local Publications
  - Inquiring News, North End Agents, The Hartford News, and Hartford Courant

**Brought to you by Industry Partners**

**DAS Small/Minority S/MBE Sam.gov Registration**

**Hands-On Certification Clinics**  
12:00 PM – 2:00 PM  
Space is Limited [15 people per clinic]. Lunch provided.

- June 21, 2023
- August 16, 2023
- September 20, 2023
- October 18, 2023
- November 15, 2023

**The Metropolitan District (MDC) Training Center**  
125 Maxim Road  
Hartford, CT 06114

**Meet with Experts. Get On-Site Help.**

Representatives from DAS Supplier Diversity Certification Unit and Connecticut APEX Accelerator (formerly CT PTAC), will be onsite to review your application for CT DAS Supplier Diversity Program SBE/MBE Certification and will assist with SAM.gov registration process that is required for state SBE certification and recertification.

- ✓ Review your application
- ✓ Assist in updating your recertification application
- ✓ Answer your questions
- ✓ And more!

**REGISTER TO ATTEND**

Space is limited. Lunch Provided. No cost to attend.

**REGISTRATION IS REQUIRED.**  
Select a date(s) to attend.

➔ **Email: Kevin Nodwell at: [kevin.nodwell@ct.gov](mailto:kevin.nodwell@ct.gov).**

You can register to attend one clinic, or more, as needed. If you register and cannot attend, please let us know in advance as space is limited.

24



# MDC's Seeds of Partnership: Transforming Local Labor Recruitment

- Attended to provide update on MDC bidding and match making opportunities
  - CCIA Annual Meeting & MCC Members Meeting
  - Greater Hartford African American Alliance (GHAAA) Weekly Meetings
  - University of Hartford Internship Event
  - Hartford Public High School – November 17<sup>th</sup>
    - MDC, District Contractors (BLD Services, Boisvert Plumbing, VMS Construction) and DOT Contractors

**MDC**

**CONTACT INFORMATION**

[themdc.org/careers/](https://themdc.org/careers/)

555 Main Street  
Hartford, CT 06103

(860) 278-7850 x3268

@MDCWater

facebook.com/themetropolitandistrict

@MDC Hartford

The Metropolitan District's (MDC) Worked-based Learning Program is a paid internship program developed in partnership with various workforce development partners to help build a strong pipeline of knowledgeable workers into the water and wastewater industries.

**PARTNERSHIPS**

- CTECS
- Gateway Community College
- Urban League of Greater Hartford
- Greater Hartford African American Alliance

**MDC WORK-BASED LEARNING PROGRAM**

PAID INTERNSHIP OPPORTUNITIES

themdc.org

**MDC**  
The Metropolitan District

**METROPOLITAN DISTRICT COMMISSION**

# MDC's Seeds of Partnership: Transforming Local Labor Recruitment

- Attended to provide update on MDC bidding and match making opportunities continued
  - Minority Construction Council (MCC) – Construction Expo & Match Maker Event
    - Bloomfield Community Center – October 6<sup>th</sup>
    - Training Alliance Partner Award / Recognition Received - [Minority Construction Council - Advancing the cause of minority contractors \(mccforct.org\)](#)
    - F.A.D. Mechanical (MBE) attended October 11<sup>th</sup> BWV pre-bid from connection made at the event
- Workforce Development relationship building, including:
  - CCIA and CTECS Work-Based Learning Seminar
  - MDC Work Based Learning Program Brochure
  - MDC, CT Pre-Apprenticeship and CT DOT - Try a Trade Program



**Try a TRADE**

**NOW OFFERING FULL SCHOLARSHIPS FOR HIGH SCHOOL SENIORS**

The best way to find out if you like something is to give it try!

Try a TRADE is a one week hands on program to do just that! Join us as we explore several different and profitable career paths through hands on learning! Students will have the opportunity to earn several certificates as well as gain knowledge and a better understanding of each trade and how to apply. Instruction may include Fall Protection, Ladder Safety, Flagger Certification, Work Zone Safety, Fire Extinguisher Safety, Silica Awareness, Concrete Work, OSHA-10 Certification, CPR/AED/First Aid Certification, Hoisting and Rigging, etc. Participants will receive Personal Protective Equipment including a Hard Hat, Safety Glasses, Work Gloves and PPE bag.

- Metropolitan District Commission
- Electricians Union
- Operating Engineers Union
- Iron Workers Union
- Carpenters Union
- Laborers Union

**PROGRAM DETAILS**  
DATES: April 8<sup>th</sup> - 12<sup>th</sup>, 2024  
TIME: 8:00 am - 2:30 pm  
LOCATION: MDC Training Center  
125 Maxim Road, Hartford, CT  
COST: FULL Scholarship for those that are accepted into the program.  
Transportation may be included.  
Space is limited - Apply Now! Scan the code or visit  
CTPAHSTP.com

SCAN ME

This program is funded by:

CONNECTICUT  
The Apprenticeship  
High School Training Program



MDC  
The Metropolitan District  
Hartford, Connecticut

# MDC's Seeds of Partnership: Transforming Local Labor Recruitment

- 30% Hartford resident workforce goal
- Match making qualified Hartford residents to Prime Contractors working for MDC in North Hartford
  - 1 Hartford residents hired by MDC Contractors in Q4
  - 7 Hartford residents in contact with MDC looking for jobs in Q4
- Work Based Learning Program coordination with local school and/or Non-Government Organizations (NGOs)
  - Coordination with E.C. Goodwin, A.I. Prince Tech., Howell Cheney Tech., and Hartford Public Schools
  - Outreach via school presentations, construction site visits, and job fairs (Learn and Earn Summer 2023 Program revamped to Work-Based Learning Program with Try a Trade Event in Q1)
- Workforce Development at MDC and student training programs (partnership with the CT Pre-apprenticeship, Ready CT and DOT)




# Hartford Labor Status

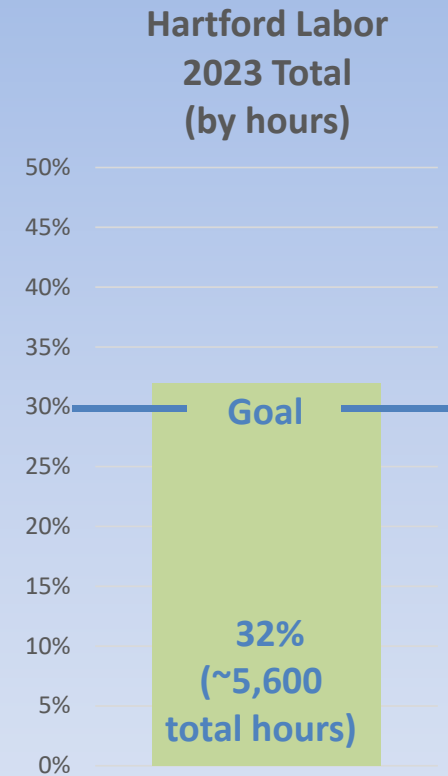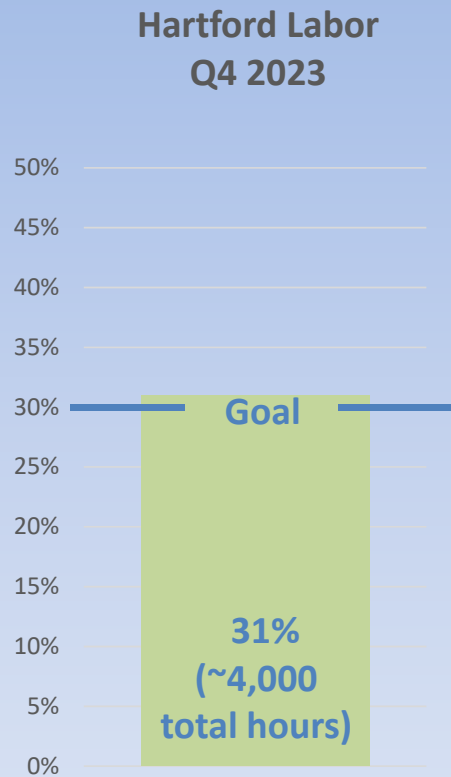

**Note:** Statistics are based on all Hartford Consent Order projects started after July 2023 under construction. 30% target based on similar City of Hartford goal on municipal projects.

# Minority/Women Business Enterprises Status

## MBE and WBE Q4 2023 (by \$)

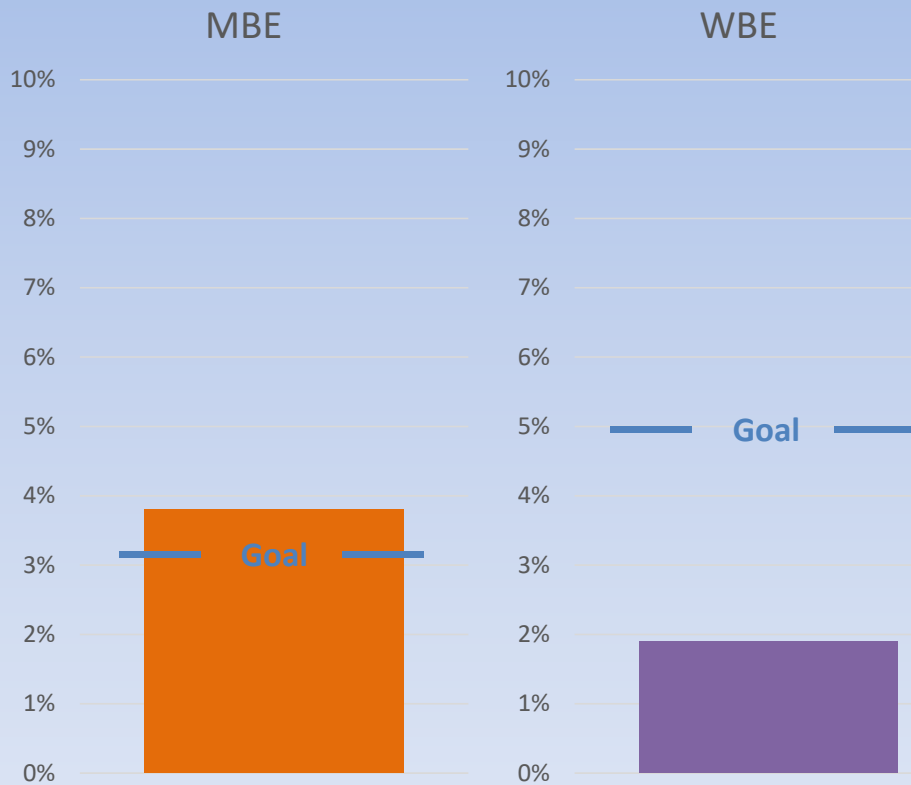


## MBE and WBE 2023 Total (by \$)



**Note:** Statistics are based on all Consent Order related projects under construction, beginning in Q3 of 2023.  
MBE and WBE targets based on CT DEEP Clean Water Fund (CWF) goals

# Clean Water Project Charge (CWPC)

Significant change in plan has **not** resulted in any additional CWPC charges than originally projected in September 2022 by receiving additional grant money from CT DEEP and deferring many projects in original Integrated Plan to the 2030s and beyond (next slide)

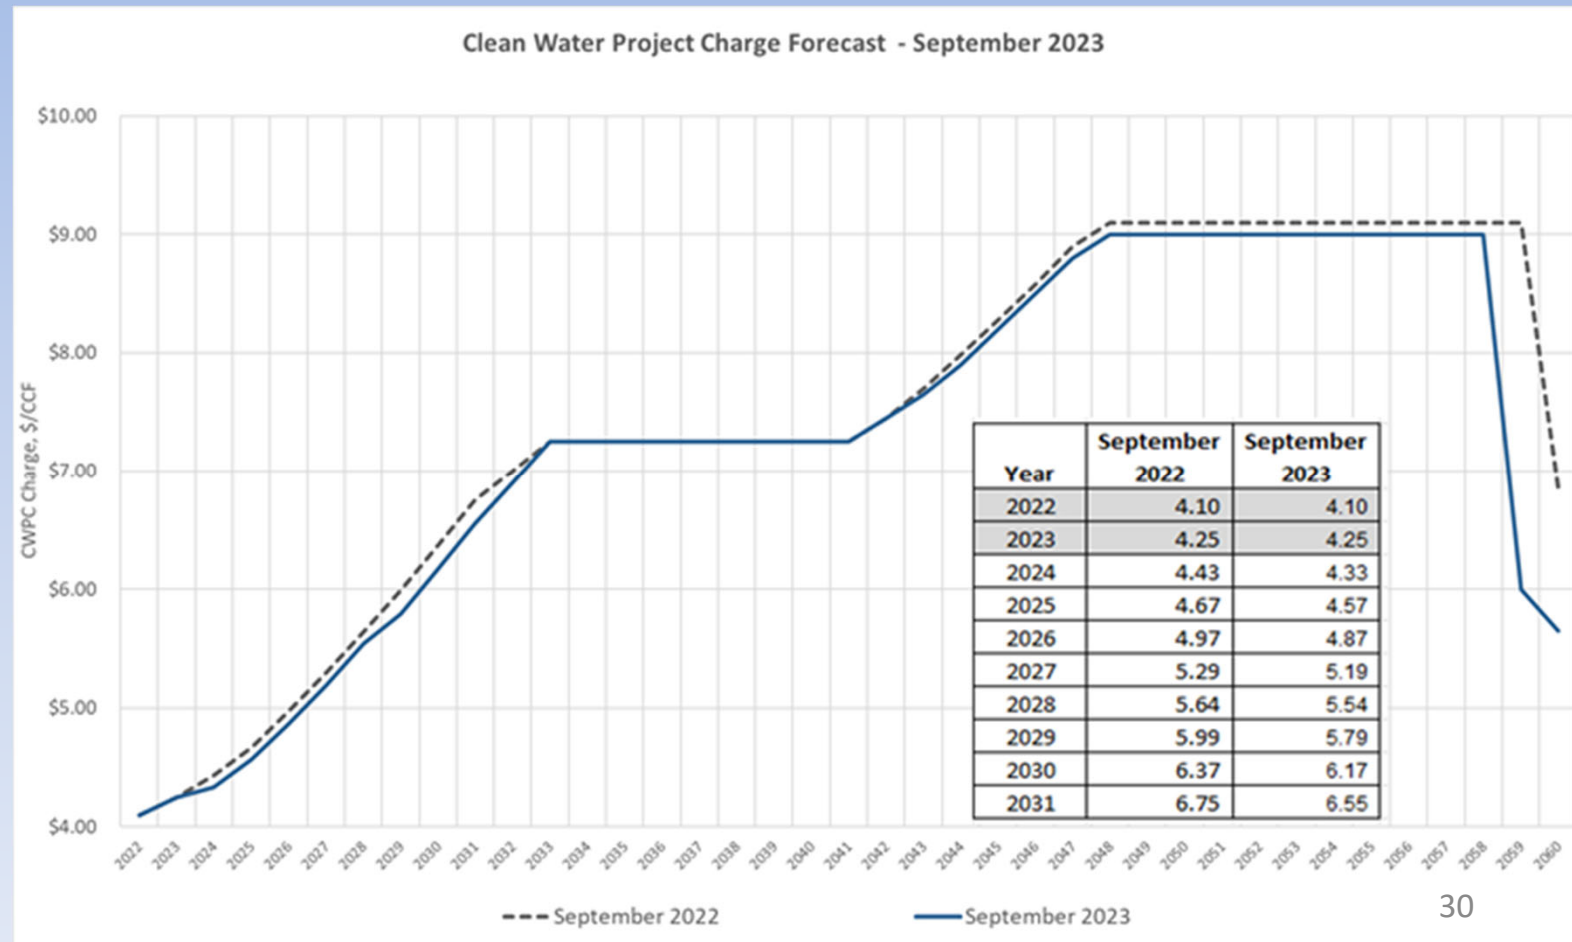

## Deferred Projects from 2018 Integrated Plan

Original Phase 1 CWP/IP Project	Original End Date	Revised End Date
SM-2 Improvements	2024	2030 - 2040
Cemetery Brook Area Large Diameter Rehab	2025	2030 - 2040
Farmington and Homestead Ave Large Diameter Rehab	2026	2030 - 2040
New North Branch Interceptor Improvements	2027	2030 - 2040
Kane Brook (S-8 & S-13)	2027	2030 - 2040
Homestead Avenue Interceptor Improvements (Design Only)	2029	2030 - 2040
Gully Brook Area Large Diameter Rehab (Part 1)	2029	2030 - 2040
Gully Brook Area Large Diameter Rehab (Part 2)	2029	2030 - 2040
N-12 Sewer Separation and CMOM	2029	2030 - 2040
South Hartford Conveyance & Storage Tunnel (SHCST) Contract 4	2029	2030 - 2040
Small Diameter Sewer Rehab Program	2029	2030 - 2040
Newington SSO Separation	2026	2030 - 2040
Wethersfield SSO Separation	2026	2030 - 2040
Franklin Avenue Area Sewer Relocations	2026	2030 - 2040
Wethersfield Trunk Sewer (Design Only)	2028	2030 - 2040

- In addition, the Downtown Tunnel was deferred to beyond 2050 (if needed)

## Closing Remarks

- Many ongoing initiatives and projects
- Many ways to **stay informed**
  - Visit - <https://themdc.org/north-hartford-sewer-improvement-projects/>
  - Via your local NRZ
- Quarterly Consent Order Meetings
  - Second Thursday of the months of March, June, September, and December
  - Each meeting will also be virtual
- Comments and Questions





# List of Acronyms

- AFSCME = American Federation of State, County and Municipal Employees
- AHNA = Asylum Hill Neighborhood Association
- BWV = Backwater Valve
- CSO = Combined Sewer Overflow
- CT DEEP = Connecticut Department of Energy and Environmental Protection
- CWF = Clean Water Fund
- CWPC = Clean Water Project Charge
- DAS = Department of Administrative Services
- DBE = Disadvantaged Business Enterprise
- EPA = Environmental Protection Agency
- GHAAA = Greater Hartford African American Alliance
- IP/CSO LTCP = Integrated Plan/CSO Long-Term Control Plan
- MBE = Minority-Owned Business Enterprise
- MCC = Minority Construction Council
- MG = Million Gallons
- NAWIC = National Association of Women in Construction
- NBPR = North Branch Park River
- NGOs = Non-Government Organizations
- NRZs = Neighborhood Revitalization Zones
- PPID = Private Property Inflow Disconnect
- Q3 = Quarter 3 (period from July 1, 2023 to September 30, 2023)
- RFP = Request for Proposal
- RFQ = Request for Qualifications
- ROW = right-of-way
- SBE = Small Business Enterprise
- SHCST = South Hartford Conveyance & Storage Tunnel
- SSES = Sanitary Sewer Evaluation Survey
- SSO = Sanitary Sewer Overflow
- WBE = Women-Owned Business Enterprise


# Common Terms & Definitions

- **Separate/sanitary sewer**
  - pipe designed to only convey wastewater
  - how sewers are built now, all member towns except Hartford
- **Storm drain**
  - pipe designed to convey only stormwater
- **Combined sewer**
  - pipe designed to convey **both** sanitary and stormwater (including catch basins)
  - How sewers were built 100 years ago
  - Issues with Combined Sewers:
    - **Dry Day:** No issues, enough capacity for household sewage (toilet, showers, etc)
    - **Wet Day:** Stormwater enters sewer (example: through catch basins). The combined sewer becomes too full, causing overflows (CSOs) into streams/rivers

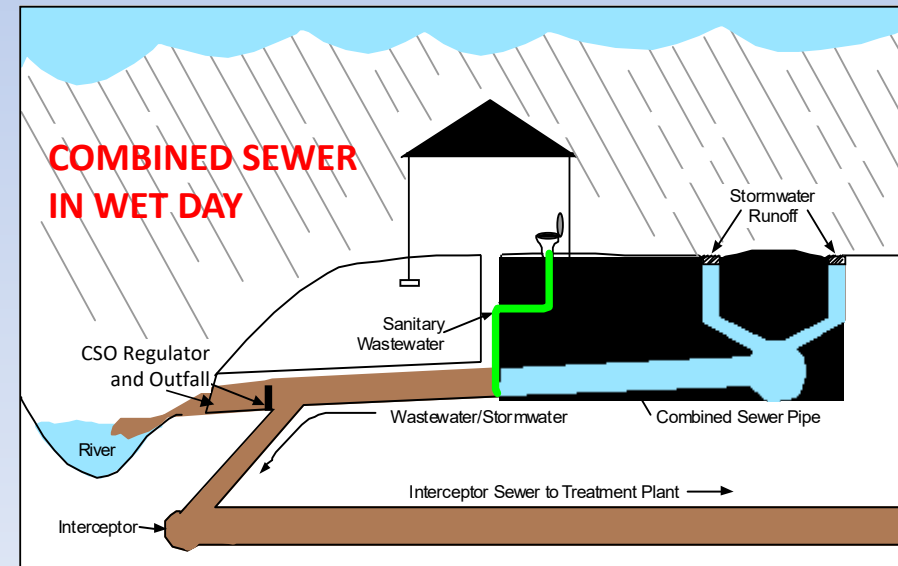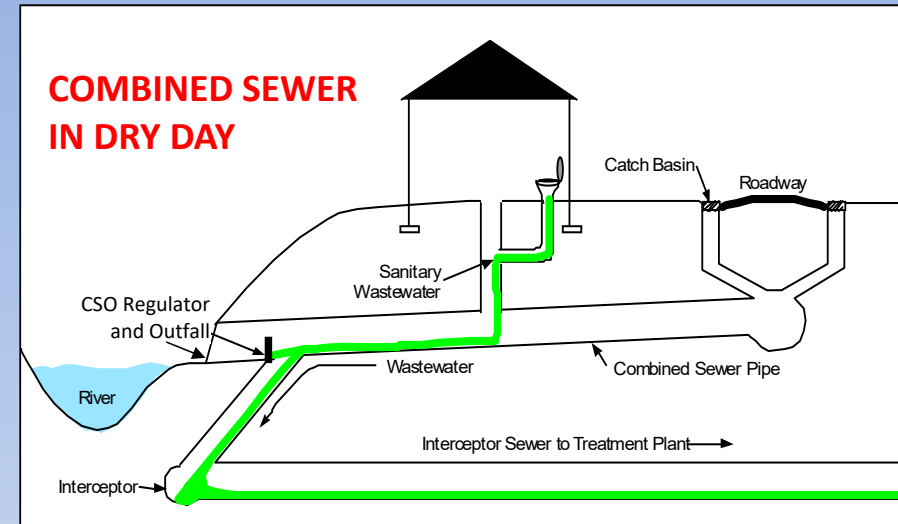

# Common Terms & Definitions

- **Lateral/House Connections**
  - Pipe (shown in red) connecting the wastewater from homes to the District's sewer main
- **Combined Sewer Overflow (CSO)**
  - condition that occurs when wet weather flows in a combined sewer system exceed the treatment capacity at the plant and/or in the pipes, causing it to discharge flow into typically a storm drain or river (via a CSO regulator and outfall)
    - Example: "N-2" and "N-4"
- **Sanitary Sewer Overflow (SSO)**
  - a condition that may occur due to blockage/clog in a pipe, broken infrastructure, or due to significant rainfall

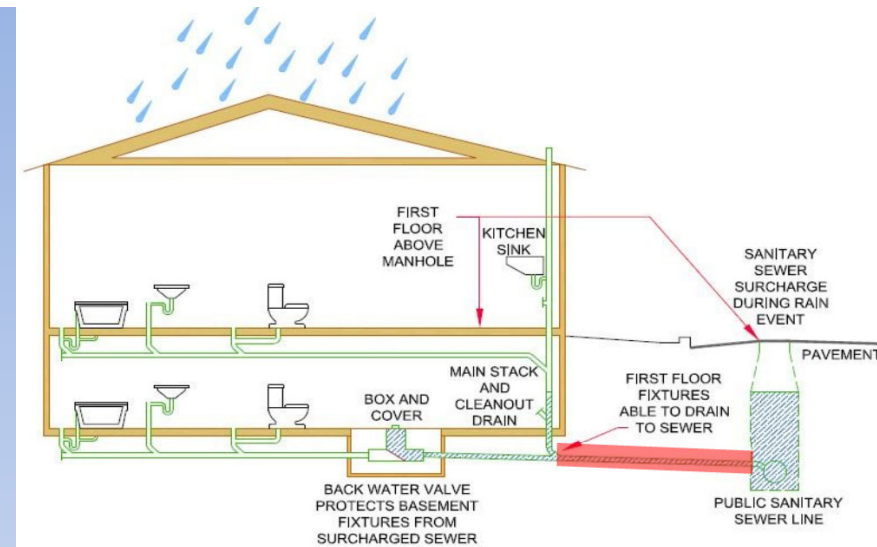

# Consent Order Projects: North Hartford Updates

Further information and regular updates on status of each North Hartford project can be found on the District's website:

- **Overall progress:** <https://themdc.org/north-hartford-sewer-improvement-projects/>
- **Expedited Sewer Separation Contracts:**
  - **Durham Street:** <https://themdc.org/north-hartford-sewer-improvement-projects/durham-street-sewer-separation/>
  - **Woodstock and Branford Streets:** <https://themdc.org/north-hartford-sewer-improvement-projects/expedited-sewer-separation-contracts-in-north-hartford/>
  - **Westland Street Area Sewer Separation:** <https://themdc.org/north-hartford-sewer-improvement-projects/westland-street-sewer-separation/>
- **Tower Ave Area Sewer Rehabilitation:** <https://themdc.org/north-hartford-sewer-improvement-projects/sewer-lateral-rehabilitation/>
- **Sewer & Lateral Rehabilitation in North Branch Park River Drainage Area:** <https://themdc.org/north-hartford-sewer-improvement-projects/sewer-lateral-rehabilitation-in-north-branch-park-river-drainage-area/>
- **Sewer & Lateral Rehabilitation in North Meadows Drainage Area (NM 5/6/7):** <https://themdc.org/north-hartford-sewer-improvement-projects/sewer-lateral-rehabilitation-in-north-meadows-drainage-area-nm-5-6-7/>
- **Sewer & Lateral Rehabilitation in Gully Brook Drainage Area:** <https://themdc.org/north-hartford-sewer-improvement-projects/sewer-lateral-rehabilitation-in-gully-brook-drainage-area/>
- **North Branch Park River Drainage Study:** <https://themdc.org/north-hartford-sewer-improvement-projects/north-branch-park-river-drainage-study/>
