


The Metropolitan District

Silas Deane Highway
Water Main Replacement
Contract: 2024B-23



Stakeholder Meeting
April 2025

Introductions

MDC:

Operations

MDC (24 hour) Command Center: (860) 278-7850 ext. 3600

Construction Inspector

Tom Franco (Kleinfelder) Cell: (631) 828-0242

Construction Services Supervisor

Randy Ross Cell: (860) 209-1318

Construction Manager

Marco Burgio Office: (860) 278-7850 ext. 3372

Project Manager

Tom Robbins Office: (860) 278-7850 ext. 3381

Communications Administrator


Julie McLaughlin Office: (860) 278-7850 ext. 3309

Contractor: Burns Construction Company

300 Sperry Avenue
Stratford, CT 06615
(203) 375-1383

Principal/Project Manager

Anthony DiVirgilio Office: (203) 375-1383
Cell: (203) 395-5314


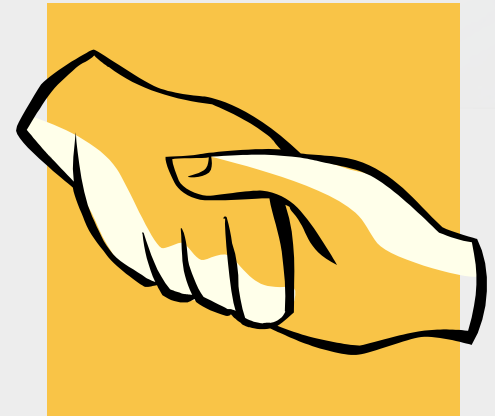


Overview/Scope of Project

Project work includes:

- Replacement of approximately 6,900 LF of 8-inch and 12-inch water pipe along Silas Deane Highway, from Parsonage Street to Mill Street, with new 8-inch and 12-inch pipe. Replacement of approximately 1,500 LF of 12-inch water pipe along Town Line Road, from Charter Road to Silas Deane Highway, with new 12-inch pipe.
- Abandonment of approximately 820 LF of existing 8-inch water pipe along Silas Deane Highway, from Parsonage Street to Mill Street, and approximately 6,100 LF of existing 12-inch water pipe along Town Line Road, from Charter Road to Silas Deane Highway, by transferring water services, hydrants, and hydrant laterals to the new pipe.
- Installation of new hydrants, new domestic and fire services, and new meter pits at properties that currently lack an existing meter pit for domestic services.
- Surface restoration work, including temporary trench paving on all streets and permanent trench paving on Silas Deane Highway. Restoration of sidewalks, curbs, driveways, yard features, and grass areas in-kind.
- The temporary and permanent restoration of trenching and disturbed surface areas, including street pavement, pavement painted striping, signal light loop detectors, sidewalk, curbs, landscaped area, driveways, etc.

Project Area (Wethersfield & Rocky Hill)

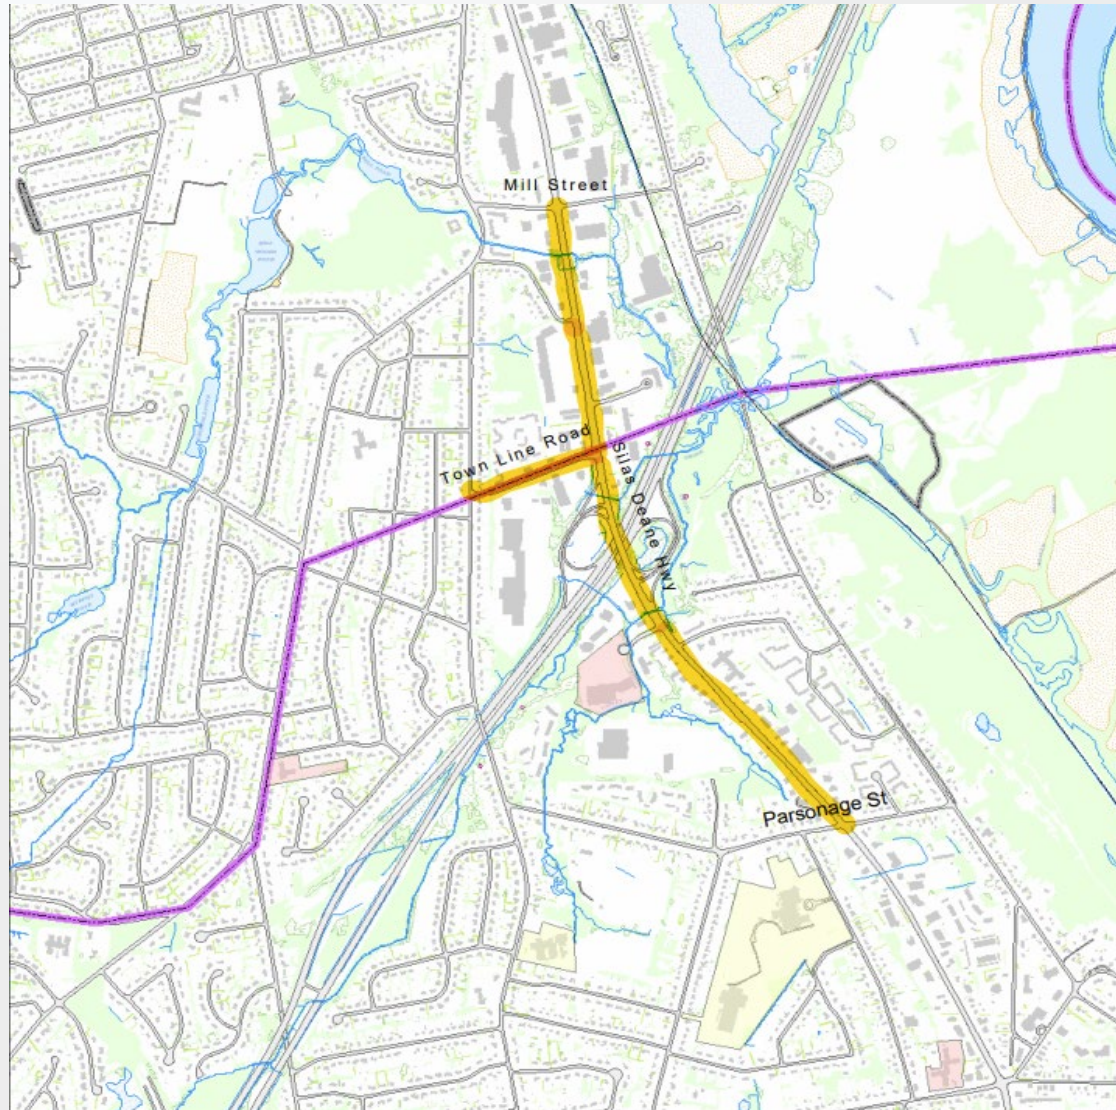

Schedule

Contract time for this project is 364 calendar days not including the “winter shutdown” period.

- Pre-construction Meeting: Wednesday March 19th, 2025.
- Notice to Proceed: Monday April 21, 2025
- Mobilization: Monday April 21, 2025
- Construction Begin: Monday April 21, 2025
- Construction Complete: Tentative, August 2026

BURNS plans to work five (5) eight (8) hour nights. Sunday-Thursday, 8:00pm-5:00am. Working hours (not night work) is Monday through Friday Between the hours of 08:30am-04:00pm.

Note: BURNS to notify the District and formally request for approval to work outside of hours mentioned.

Traffic Control

- There are planned traffic patterns for this project.
- In addition to the traffic control plans provided in the contract documents, the contractor may submit an alternate plan for review and approval by the MDC and CT DOT prior to implementation. If an alternate plan is approved, the attached plans will be updated.
- Work zone area varies along project.
- Impact attenuators to be used and are found within approved Traffic Management Plans.



Outreach

- Weekly project emails & periodic meetings will be conducted as needed.
- Notifications will be sent out ahead of each phase of work.



Thank you for joining us today.

Discussion and Questions?
