



The Metropolitan District
water supply · environmental services · geographic information

Memorandum

To: Graham Stevens, CT DEEP
Co-Chair Senator Rick Lopes, Environment Committee
Co-Chair Representative John-Michael Parker, Environment Committee
Co-Chair Representative Eleni Kavros DeGraw, Planning & Development Committee
Co-Chair Senator MD Rahman, Planning & Development Committee

From: Susan Negrelli, P.E., MDC *SN*

Date: July 31, 2026

Re: **MDC Public Act No. 23-204 / House Bill No. 6941 Monthly Report – June 2026**

cc: Scott Jellison, P.E., MDC
Chris Levesque, P.E., MDC
Michael Curley, P.E., MDC
Jason Waterbury, P.E., MDC
Mary Manning, P.E., MDC
Dave Ruddy, MDC
Alex Dobiecki, P.E., MDC
Jeremy Galeota, P.E., MDC
Jason Bretemps, MDC
Nisha Patel, CT DEEP
Ivonne Hall, CT DEEP
Stacy Pappano, CT DEEP
Ann Straut, CT DEEP

The purpose of this memorandum is to provide a monthly report to CT DEEP and the State General Assembly's Environment Committee and Planning and Development Committee on the below three program items dealing with the repairs and improvements to the Hartford sewershed:

- a description of any repairs and improvements begun or completed in the previous month under the program developed pursuant to this section;
- an itemized accounting of expenditures relating to such repairs and improvements; and

- a list of any repairs and improvements that the District has begun but has been unable to complete due to permitting issues, and the nature of any such issues.

The initial report submitted on January 31, 2024 included a detailed description of the scope of all projects anticipated to be undertaken pursuant to the program and an estimated schedule for commencement and completion of each project. After submitting such initial report, the District shall not be required to submit a report for any month in which it did not undertake repairs or improvements pursuant to such program.

June 2026 Report:

As shown on Table 1, attached, for the month of June 2026, the District completed the following improvements to its existing sewer collection system and private property sewage system assets in the Hartford sewershed. This is also shown on **Figure 1**, which summarizes improvements completed in June 2026 in comparison to total improvements completed to date in 2026, and since program inception in late 2023.

- 3,397 LF of CIPP mainline rehabilitated combined or sanitary sewers
- 8 point repairs (performed by District Operations crews)
- 27 sewer laterals replaced
- 113 sewer laterals inspected
- 5 new storm laterals installed
- 7,321 LF of sewer laterals rehabilitated with a CIPP liner, representing 196 properties
- 107 properties with surcharge protection devices installed (i.e. backwater valves, sump pumps, etc.)
- 16 properties where internal inflow was disconnected from the sewer lateral for surcharge protection

As a result of an internal audit of work completed, District staff determined that the quantity of private properties disconnected had been under-reported in previous reports to date. As such, the quantities for both program total to date and previous year (2025) have been adjusted in Figure 1, and have been discussed in the District's June 11 public meeting.

As shown on **Table 1**, attached, during the month of June the District expended \$4,211,607 on the existing collection system and private property sewer improvements that will benefit the residents of Hartford. It should be noted that this value is expenditures paid, and due to invoicing submission schedules, may not directly correlate to work performed in June 2026. Costs presented do not include internal costs associated with the District's program management consultant, District labor, or costs associated with repairs completed by District operations crews. Additionally, expenditures on the South Hartford Consolidation and Storage Tunnel projects (Contract 3) are not included.

As of June 30, 2026, the District is currently waiting for 43 permit approvals for work that will protect residents from potential sewer/stormwater backups and remove excess flows from the

system. The removal of this excess stormwater or groundwater from connections to the District's collection system is a key component in reducing potential surcharges in the District's collection system. **Table 2**, attached, summarizes the private property permits that are pending municipal approval. The District continues to actively collaborate with the City of Hartford on pending permits and the permit process. There is a shared expectation that once the District completes the \$170 million Clean Water/Integrated Plan project separation work, properties will be better protected from both sewer backups and stormwater.

For additional information regarding the specifics of individual projects, please refer to the District's website at <https://themdc.org/>.



Table 1: Summary of Repairs, Improvements, and Expenditures
Public Act No. 23-204 / House Bill No. 6941 Monthly Report for
June 2026 Activities

July 31, 2026

Project	District Operations Staff	On-Call Sewer/Paving Program Coordination	NBPR Area Sewer and Lateral Rehabilitation/Repair (2023B-60)	Gully Brook Area Sewer & Lateral Rehabilitation/Repair (2023B-61)	North Meadows Area Sewer & Lateral Rehabilitation/Repair (2023B-62)	West Hartford SSES Implementation (2024B-19)	Large Diameter Phase 3A (Part 1) (18-in to 21-in Brick Rehab)	Chadwick & Deerfield (2024B-13)	Backwater Valve/Private Property Inflow Disconnection	House Connection Program	Total
<i>Mainline CIPP (LF)</i>	0	0	0	0	3,078	319	0	0	0	0	3,397
<i>Tophat (EA)</i>	0	0	0	0	0	0	0	0	0	0	0
<i>Sewermain installed or replaced (LF)</i>	0	0	0	0	0	0	0	0	0	0	0
<i>Sewer lateral replacement (EA)</i>	0	0	0	0	0	0	0	0	0	27	27
<i>Sewer laterals inspected (EA)</i>	0	0	0	0	45	0	0	0	68	0	113
<i>Sewer lateral lining (EA)</i>	0	31	41	24	0	58	0	39	0	3	196
<i>Sewer lateral lining (LF)</i>	0	1,455	1,371	865	0	2,673	0	767	0	190	7,321
<i>Point repairs (EA)*</i>	8	0	0	0	0	0	0	0	0	0	8
<i>New storm main (LF)</i>	0	0	0	0	0	0	0	0	0	0	0
<i>New storm lateral (EA)</i>	0	5	0	0	0	0	0	0	0	0	5
<i>Backwater valve/surcharge protection (# of properties)</i>	0	0	0	0	0	0	0	0	107	0	107
<i>Private property internal disconnect (# of properties)</i>	0	0	0	0	0	0	0	0	16	0	16
<i>Expenditures</i>	\$0**	\$1,407,381	\$65,879	\$466,895	\$878,818	\$334,021	\$127,115	\$62,114	\$869,384		\$4,211,607

*As of April 1, 2024, only point repairs where subsequent CIPP is not performed on the sewer will be reported

**Cost for this work is internal District costs and therefore not included



Table 2: Pending Private Property Permits
Public Act No. 23-204 / House Bill No. 6941 Monthly Report for
June 2026 Activities

July 31, 2026

Town	Number of Permits Pending Approval
Bloomfield	1
Hartford	36
Newington	0
West Hartford	4
Windsor	2
Total	43

Figure 1: Summary of Repairs, Improvements, and Expenditures for 2026
Public Act No. 23-204 / House Bill No. 6941 Monthly Report for
June 2026 Activities

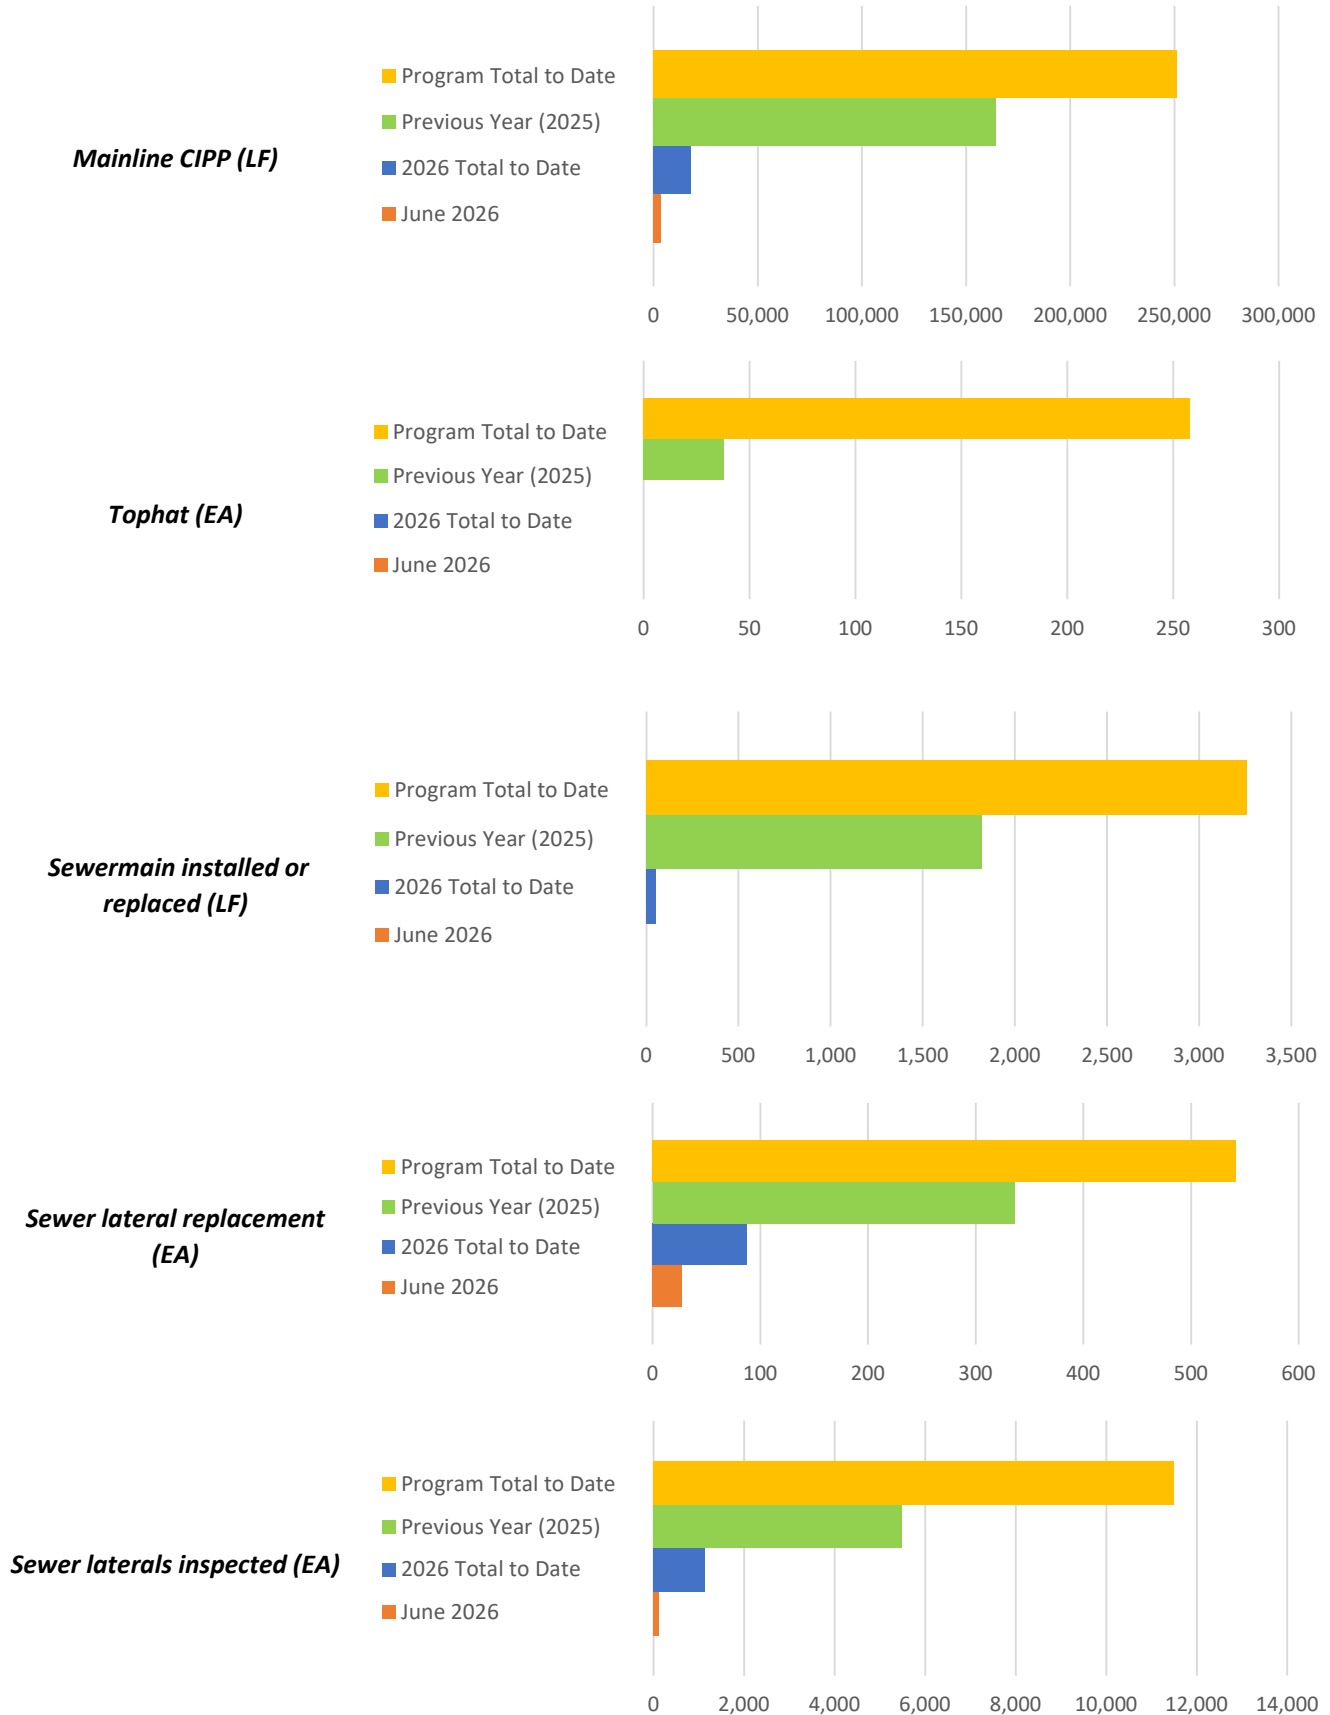


Figure 1: Summary of Repairs, Improvements, and Expenditures for 2026
Public Act No. 23-204 / House Bill No. 6941 Monthly Report for
June 2026 Activities

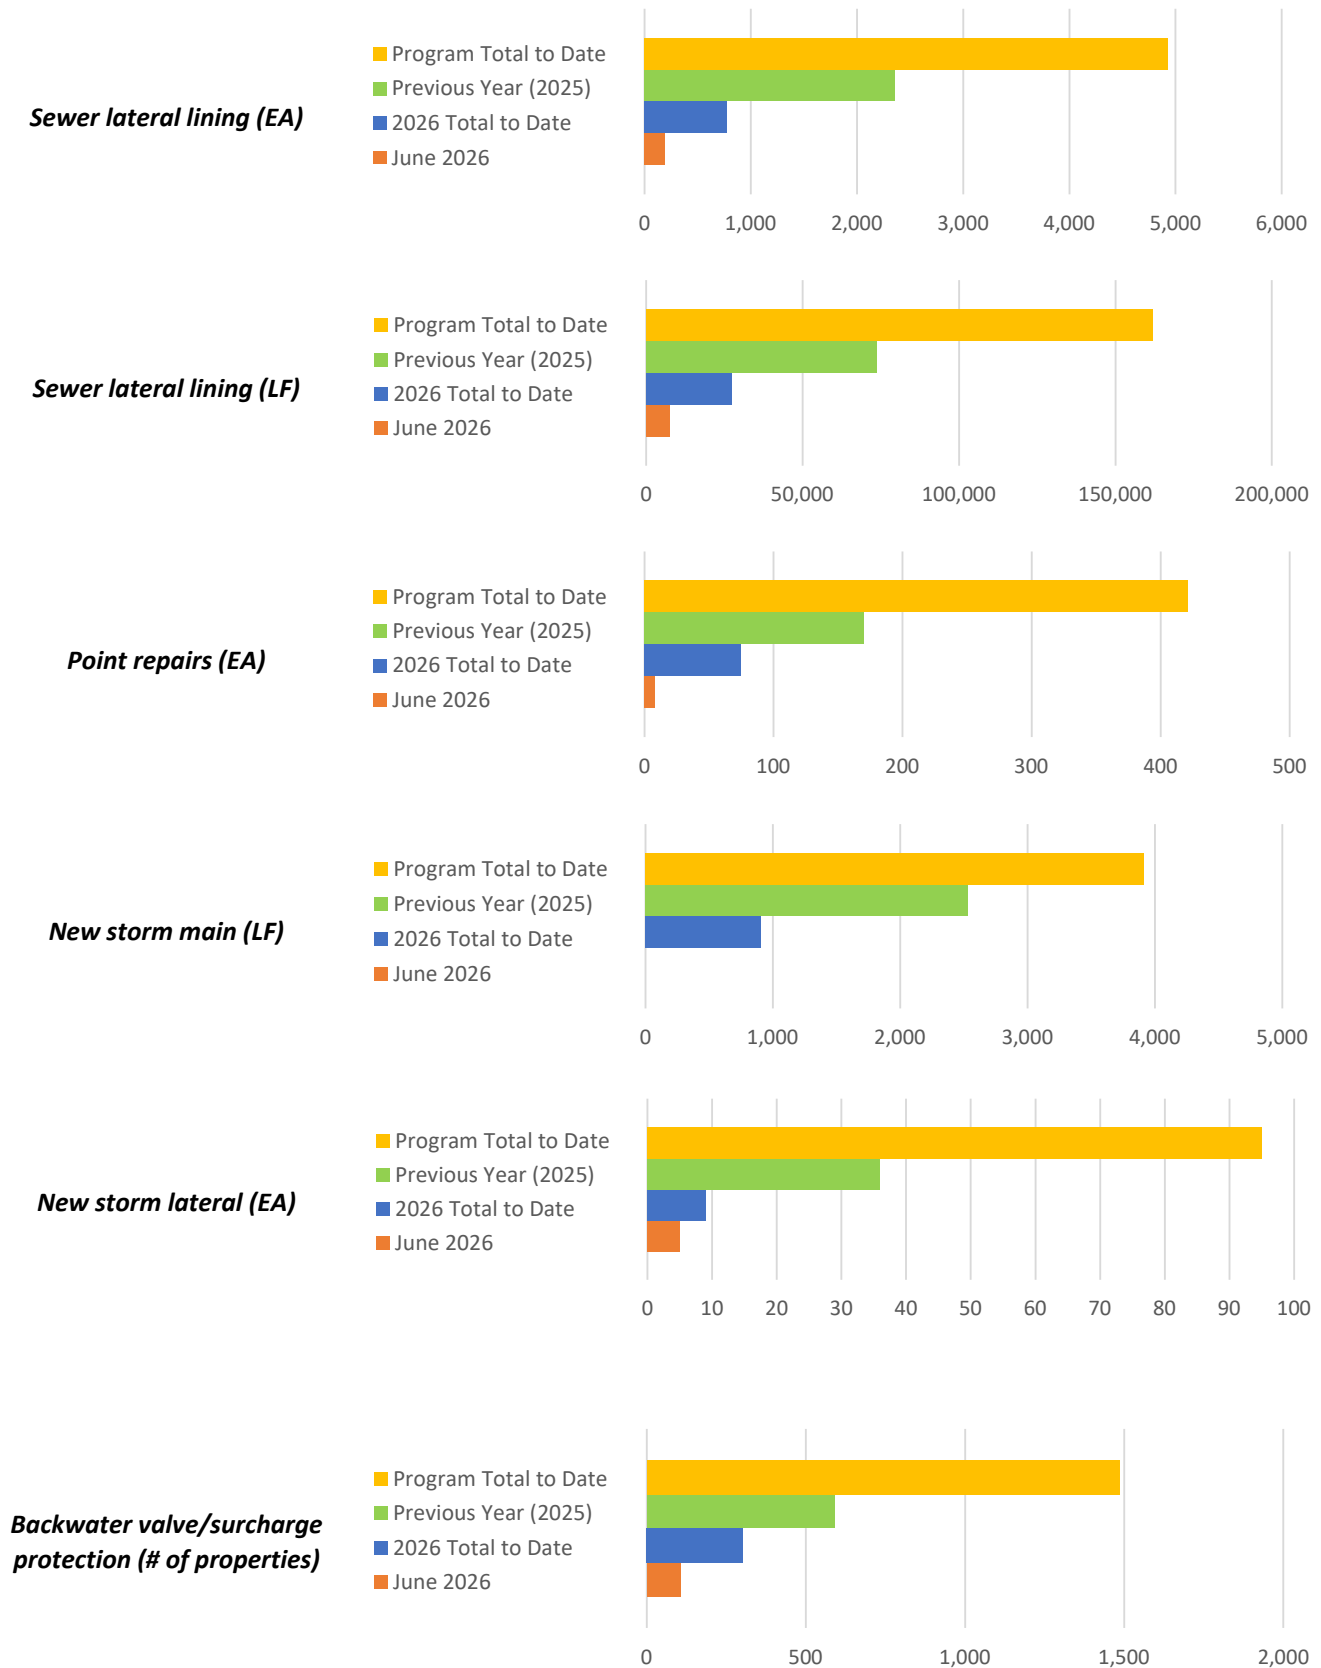


Figure 1: Summary of Repairs, Improvements, and Expenditures for 2026
Public Act No. 23-204 / House Bill No. 6941 Monthly Report for
June 2026 Activities

***Private property internal
disconnect (# of properties)***

**** Note: Program total to date
for this work has been
updated, based on updated
accounting***

